
Map: how work and data move between departments

Ravashing Exhibitions & Events, Build side · 6 Nov 2026 · Confidential

Line style — confirmed · told, not confirmed · assumed

Colour = channel — Paper printout · WhatsApp · Email / shared files · Excel / list · Phone / in person · Talk that bypasses the PM

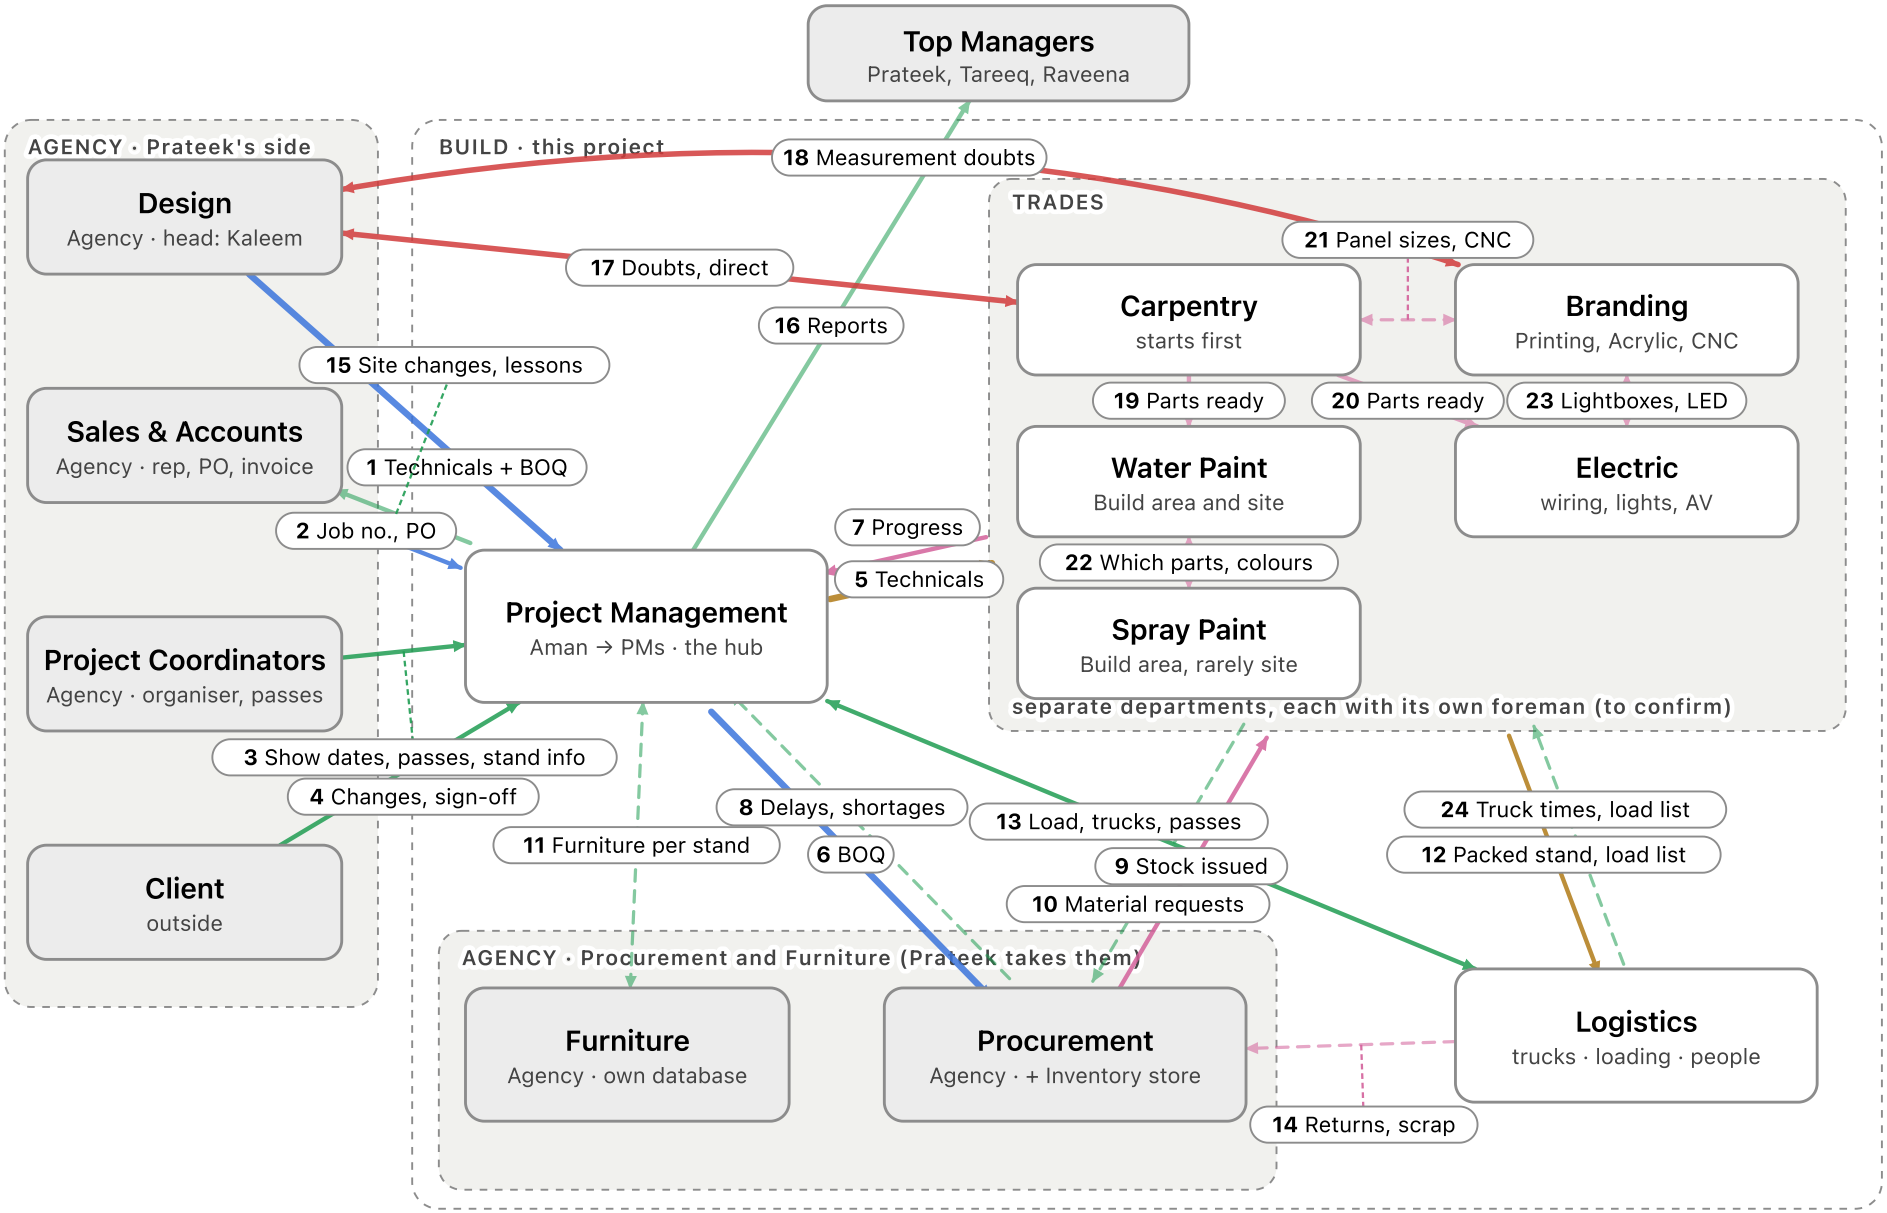

Key to the numbered flows

● confirmed by someone doing that work ◐ told to us, not yet confirmed ○ our guess from similar companies. A ? after a channel means the channel is a guess. Team sizes are guesses.

#	From	To	Data	Channel	Who reads it on arrival (our guess)	Status
1	Design	Project Management	Technicals (3D design, 2D plan, colour codes, item and AV lists, special elements) and the BOQ	Email / shared files? WhatsApp?	The PM who owns the stand; Aman sees it too	● Confirmed by someone doing that work
2	Sales & Accounts	Project Management	The rep gives the go-ahead to release; PO and advance received, job number opened	Email / shared files? WhatsApp?	The PM who owns the stand; Aman	◐ Told by someone else, not yet confirmed
3	Project Coordinators	Project Management	Show dates, build-up windows, passes, organiser approvals, and stand information (the Sales team sends stand information too)	WhatsApp	The PMs on that show; Aman	◐ Told by someone else, not yet confirmed
4	Client	Project Management	Change requests during the build; walk-through and sign-off	WhatsApp	The PM who owns the stand	◐ Told by someone else, not yet confirmed
5	Project Management	the five trades	Printed technicals pack for Carpentry, Water Paint, Spray Paint, Electric and Branding	Paper printout? WhatsApp?	Each trade's foreman, who passes it to the workers	● Confirmed by someone doing that work
6	Project Management	Procurement	BOQ: list of items and quantities (Prateek's note says there is no per-stand BOQ: Procurement reads the 3D render; open)	Email / shared files? Excel / list?	The buyer or store keeper who does the stock check	● Confirmed by someone doing that work
7	the five trades	Project Management	Progress of each stand and people counts per trade; also what goes back up to the PM: build schedule, site dates, client questions	Phone / in person? WhatsApp?	The PM who owns the stand	◐ Told by someone else, not yet confirmed
8	Procurement	Project Management	Missing items and late deliveries	WhatsApp? Phone / in person?	The PM who owns the stand	○ Assumed from similar companies
9	Procurement	the five trades	Items and materials from the store for the five trades	Phone / in person? Paper printout?	The foreman, and the workers who collect from the store	◐ Told by someone else, not yet confirmed
10	the five trades	Procurement	Requests for items not on the BOQ, such as unique client items	WhatsApp? Phone / in person?	The buyer or store keeper	○ Assumed from similar companies
11	Project Management	Furniture (both ways)	Which furniture each stand needs; ready or short (Furniture is Agency side)	WhatsApp? Excel / list?	The furniture coordinator; the PM	○ Assumed from similar companies
12	the five trades	Logistics	Dismantled, labelled stand parts and a signed load list	Paper printout? Phone / in person?	The transport planner or dispatcher; loaders use the load list	◐ Told by someone else, not yet confirmed
13	Project Management	Logistics (both ways)	Ready-to-load signal; furniture and stock to load, also before the site; truck left, reached, offloaded; venue slots and passes handed down from the Coordinators	WhatsApp Phone / in person	The transport planner or dispatcher; the PM	◐ Told by someone else, not yet confirmed

#	From	To	Data	Channel	Who reads it on arrival (our guess)	Status
14	Logistics	Procurement	Items back from the show; scrap	Phone / in person?	The store keeper (Inventory)	○ Assumed from similar companies
15	Project Management	Sales & Accounts	Updates go to Sales and the top managers (told); site changes for the final invoice; lessons learned	WhatsApp? Excel / list?	Accounts (final invoice) and Sales	◐ Told by someone else, not yet confirmed
16	Project Management	Top Managers	Updates to the boss (told, not clear which top manager); progress and status reports	WhatsApp? Excel / list?	Top Managers	◐ Told by someone else, not yet confirmed
17	Design	Carpentry (both ways)	Doubts about a drawing are sometimes answered by Design directly; the PM may not hear about the change	Phone / in person? WhatsApp?	The Carpentry foreman; the designer at Design who answers	◐ Told by someone else, not yet confirmed
18	Design	Branding (both ways)	Questions to Design about measurements, besides the drawings that come from the PM	WhatsApp?	The Branding foreman or designer; Design	◐ Told by someone else, not yet confirmed
19	Carpentry	Water Paint	Some parts are ready, so Paint starts primer	Phone / in person?	The Paint foreman	◐ Told by someone else, not yet confirmed
20	Carpentry	Electric	Some parts are ready, so Electric starts fixing	Phone / in person?	The Electric foreman	◐ Told by someone else, not yet confirmed
21	Carpentry	Branding (both ways)	Sizes the graphics must fit; CNC cut files and cut parts for Carpentry (CNC sits under Branding)	Phone / in person?	The Branding foreman; the Carpentry foreman	○ Assumed from similar companies
22	Water Paint	Spray Paint (both ways)	Which parts are sprayed and which are water-painted; colour codes; order of work on a stand	Phone / in person?	The Water Paint and Spray Paint heads	○ Assumed from similar companies
23	Electric	Branding (both ways)	Cut-outs and power points for lightboxes and LED graphics; sizes	Phone / in person?	The Electric and Branding heads	○ Assumed from similar companies
24	Logistics	the five trades	Truck schedule and loading times to the trades; the trades pack to the load list	WhatsApp? Phone / in person?	Each trade's foreman	○ Assumed from similar companies

Details by department

● confirmed by someone doing that work ◐ told to us, not yet confirmed ○ our guess from similar companies. A ? after a channel means the channel is a guess. Team sizes are guesses.

Flow numbers (#) match the map. The key on the previous pages gives the full wording, the channel, who reads it and the status.

Project Management

Hub between Agency and Build: everything crosses through the PM (Prateek). Four PMs plus Aman; no assistants; no standard Excel list. Each PM owns individual stands; Aman allocates them and arranges outside help. Runs the site. Also coordinates furniture and inventory with Logistics, before the site too.

Team size (our guess): Aman plus 3 PMs (HR chart, 6 Nov); outside PMs at peak, number unknown

PEOPLE AND HIERARCHY

- ◐ Top Managers, 3 people (see both halves)
  - ● General Manager above Production
    - ● Aman, head manager of the PMs: allocates stands, arranges outside help
      - ● Project Managers: 3 listed with Aman, each owns stands
      - ● Production Coordination, 2 people, between the PMs and the divisions: role not known
- ◐ No assistants for PMs (told)
- ◐ Outside PMs hired at peak times, number unknown

DATA MANAGER: WHO KEEPS THE RECORDS

● Each PM keeps their own stand list in Excel; there is no standard list (told)

○ Aman probably collects an overview

NEEDS (RECEIVES)

#1 ● **Design**: Technicals + BOQ

#2 ◐ **Sales & Accounts**: Job no., PO

#3 ◐ **Project Coordinators**: Show dates, passes, stand info

#4 ◐ **Client**: Changes, sign-off

#7 ◐ **the five trades**: Progress

#8 ○ **Procurement**: Delays, shortages

#11 ○ **Furniture**: Furniture per stand

#13 ◐ **Logistics**: Load, trucks, passes

CREATES

● Stand list, one Excel per PM

● Site status updates (WhatsApp)

◐ Printed technicals pack for each trade

◐ Handover sheet

◐ Job file, photos, lessons learned

PASSES ON (SENDS)

#5 ● **the five trades**: Technicals

#6 ● **Procurement**: BOQ

#11 ○ **Furniture**: Furniture per stand

#13 ◐ **Logistics**: Load, trucks, passes

#15 ◐ **Sales & Accounts**: Site changes, lessons

#16 ◐ **Top Managers**: Reports

KEEPS RECORDS IN

● Excel stand lists, one per PM

● WhatsApp groups for stands and for site

◐ Printouts of technicals

Carpentry

Starts first, together with Branding. Builds the structure and the stand mock-up at the Build area. Foremen rarely go to site. Keeps no data of its own: the PMs keep it (told, 6 Nov).

Team size (our guess): 1 foreman plus 24 (HR chart)

PEOPLE AND HIERARCHY

- ● Foreman, 1: head of Carpentry
  - ● Three senior carpenters; one runs a machine
    - ● Carpenters, 21
- ◐ Outside carpentry labour at peak, number unknown
- ◐ Labour-record person, 1, shared with Water Paint
- ● Above the foreman: Production Coordination and Aman

DATA MANAGER: WHO KEEPS THE RECORDS

◐ Nobody in Carpentry: the PMs keep the information (told). The labour-record person keeps labour information

NEEDS (RECEIVES)

#5 ● **Project Management**: Technicals
#9 ◐ **Procurement**: Stock issued
#17 ◐ **Design**: Doubts, direct
#21 ○ **Branding**: Panel sizes, CNC
#24 ○ **Logistics**: Truck times, load list

CREATES

◐ Structure parts
◐ Stand mock-up
◐ Load list (with Logistics)
◐ Progress updates

PASSES ON (SENDS)

#7 ◐ **Project Management**: Progress
#10 ○ **Procurement**: Material requests
#12 ◐ **Logistics**: Packed stand, load list
#17 ◐ **Design**: Doubts, direct
#19 ◐ **Water Paint**: Parts ready
#20 ◐ **Electric**: Parts ready
#21 ○ **Branding**: Panel sizes, CNC

KEEPS RECORDS IN

◐ Labour information, partly (one person hired)
○ Job or cut lists
○ WhatsApp groups

Water Paint

Water Paint department: water paint and primer once parts are ready, at the Build area and on site too. Spray Paint is a separate department.

Team size (our guess): 9 water painters (HR chart); no head named

PEOPLE AND HIERARCHY

- ○ Head of Water Painter: not named on the HR chart
  - ● Water painters, 9
- ○ Outside painters, ≈ 4–15 at peak (guess)
- ◐ Labour-record person, 1, shared with Carpentry
- ● Above: Production Coordination and Aman

DATA MANAGER: WHO KEEPS THE RECORDS

◐ The same labour-record person keeps labour information
○ Water Paint: nobody else known

NEEDS (RECEIVES)

#5 ● **Project Management**: Technicals
#9 ◐ **Procurement**: Stock issued
#19 ◐ **Carpentry**: Parts ready
#22 ○ **Spray Paint**: Which parts, colours
#24 ○ **Logistics**: Truck times, load list

CREATES

◐ Primed and painted parts
◐ Progress updates
○ Paint usage record

PASSES ON (SENDS)

#7 ◐ **Project Management**: Progress
#10 ○ **Procurement**: Material requests
#12 ◐ **Logistics**: Packed stand, load list
#22 ○ **Spray Paint**: Which parts, colours

KEEPS RECORDS IN

◐ Labour information (shared person with Carpentry)
◐ Colour codes, from the technicals

Spray Paint

Separate department from Water Paint. Mostly at the Build area, rarely on site.

Team size (our guess): 3 including the head (HR chart)

PEOPLE AND HIERARCHY

- ● Head of Spray Painter, 1
  - ● Spray painters, 2
- ○ Outside spray painters at peak (not known)
- ● Above: Production Coordination and Aman

DATA MANAGER: WHO KEEPS THE RECORDS

○ The foreman keeps colours, spray schedule and progress notes

NEEDS (RECEIVES)

#5 ● **Project Management**: Technicals
#9 ◐ **Procurement**: Stock issued
#22 ○ **Water Paint**: Which parts, colours
#24 ○ **Logistics**: Truck times, load list

CREATES

○ Sprayed parts
○ Progress updates

PASSES ON (SENDS)

#7 ◐ **Project Management**: Progress
#10 ○ **Procurement**: Material requests
#12 ◐ **Logistics**: Packed stand, load list
#22 ○ **Water Paint**: Which parts, colours

KEEPS RECORDS IN

○ Colour codes, from the technicals
○ Spray area schedule

Electric

Joins once parts are ready. Small electric fixing at the Build area, with no progress update; progress is tracked on site, by the PMs. AV and lighting are outsourced. Orders material from Procurement (told).

Team size (our guess): 7 including the foreman (HR chart); AV and lighting outsourced

PEOPLE AND HIERARCHY

- ● Foreman, 1: head of Electric
  - ● Senior electrician, 1
    - ● Electricians, 5
- ◐ AV and lighting technicians: completely outsourced (told)
- ◐ No helpers (told)
- ● Above: Production Coordination and Aman

DATA MANAGER: WHO KEEPS THE RECORDS

◐ Nobody: the PMs track on-site progress. There is no progress update from the Build area (told)

NEEDS (RECEIVES)

#5 ● **Project Management**: Technicals
#9 ◐ **Procurement**: Stock issued
#20 ◐ **Carpentry**: Parts ready
#23 ○ **Branding**: Lightboxes, LED
#24 ○ **Logistics**: Truck times, load list

CREATES

◐ Wired, lit, tested stand
◐ Progress updates
○ Test record

PASSES ON (SENDS)

#7 ◐ **Project Management**: Progress
#10 ○ **Procurement**: Material requests
#12 ◐ **Logistics**: Packed stand, load list
#23 ○ **Branding**: Lightboxes, LED

KEEPS RECORDS IN

○ Electrical list and plan
○ Equipment (lights, cables) record

Branding

Branding department with three sub-departments: Graphics, CNC and Logo. Gets a zip file from Design. Makes prints and fits graphics on site. Who does the graphic mock-up and print proof is open: Prateek's note puts them with Design (Agency), the print itself with Build.

Team size (our guess): 5 plus the head: Printing 3, Acrylic 1, CNC 1 (HR chart)

PEOPLE AND HIERARCHY

- ● Head of Printing, Acrylic and CNC: sits under the General Manager
  - ● Printing (graphics), 3
  - ● Acrylic, 1
  - ● CNC, 1
- ○ Logo: not on the HR chart; assumed to be acrylic work
- ○ Outside graphic labour at peak, number unknown

DATA MANAGER: WHO KEEPS THE RECORDS

○ The head of Branding, or the designer / prepress person, keeps print files and print orders

NEEDS (RECEIVES)

#5 ● **Project Management**: Technicals
#9 ◐ **Procurement**: Stock issued
#18 ◐ **Design**: Measurement doubts
#21 ○ **Carpentry**: Panel sizes, CNC
#23 ○ **Electric**: Lightboxes, LED
#24 ○ **Logistics**: Truck times, load list

CREATES

◐ Graphic mock-up and logo mock-up
◐ Printed panels, banners, stickers, lightbox fabric
○ Print files

PASSES ON (SENDS)

#7 ◐ **Project Management**: Progress
#10 ○ **Procurement**: Material requests
#12 ◐ **Logistics**: Packed stand, load list
#18 ◐ **Design**: Measurement doubts
#21 ○ **Carpentry**: Panel sizes, CNC
#23 ○ **Electric**: Lightboxes, LED

KEEPS RECORDS IN

○ Print files and versions
◐ Status for the PM

Logistics

Comes in when every department is ready. Loads, moves stands to the event, and moves people. Not yet confirmed as a team of its own.

Team size (our guess): 7 including the head, Transport (HR chart); hired trucks at peak (guess)

PEOPLE AND HIERARCHY

- ● Head of Transport
  - ● Drivers and loaders, 6
- ○ Who plans the trucks? (to find out)
- ○ Hired trucks and drivers, at peak
- ○ Freight agents for overseas jobs
- ● Above: Production Coordination and Aman

DATA MANAGER: WHO KEEPS THE RECORDS

○ The transport planner / dispatcher keeps bookings, load lists and delivery notes

NEEDS (RECEIVES)

#12 ◐ **the five trades**: Packed stand, load list
#13 ◐ **Project Management**: Load, trucks, passes

CREATES

◐ Truck schedule
◐ Load list (with Carpentry)
○ Delivery notes
○ Transport and return records

PASSES ON (SENDS)

#13 ◐ **Project Management**: Load, trucks, passes
#14 ○ **Procurement**: Returns, scrap
#24 ○ **the five trades**: Truck times, load list

KEEPS RECORDS IN

○ Truck bookings
○ Driver and vehicle records

Design

Agency. Releases technicals and answers doubts. Head designer: Kaleem, who OKs graphic mock-ups. Prateek's note: the graphic mock-up and print proof are agency work under the Head of Design.

NEEDS (RECEIVES)

#17 ◐ **Carpentry**: Doubts, direct
#18 ◐ **Branding**: Measurement doubts

PASSES ON (SENDS)

#1 ● **Project Management**: Technicals + BOQ
#17 ◐ **Carpentry**: Doubts, direct
#18 ◐ **Branding**: Measurement doubts

Sales & Accounts

Agency. The rep (sales) owns the client and gives the go-ahead to release the build. Opens the job number, receives the PO and advance, issues the final invoice against site changes.

NEEDS (RECEIVES)

#15 ◐ **Project Management**: Site changes, lessons

PASSES ON (SENDS)

#2 ◐ **Project Management**: Job no., PO

Project Coordinators

Agency. Handle organiser and venue approvals and passes. Build depends on their dates.

NEEDS (RECEIVES)

Nothing known yet.

PASSES ON (SENDS)

#3 ◐ **Project Management**: Show dates, passes, stand info

Client

Outside. Asks for changes, signs off at handover. Often in a WhatsApp group with Sales and the PM.

NEEDS (RECEIVES)

Nothing known yet.

PASSES ON (SENDS)

#4 ◐ **Project Management**: Changes, sign-off

Top Managers

Three people: Prateek, Tareeq and Raveena (Prateek via Narendra, 6 Nov). They see both Agency and Build. What they look at is unknown (ask Prateek).

NEEDS (RECEIVES)

#16 ◐ **Project Management**: Reports

PASSES ON (SENDS)

Nothing known yet.

Notes for Narendra only


Take this page out before showing the map to anyone else.

- **Design doubts bypass the PM.** Red lines show talks that skip the PM. In the case Ali described, Carpentry changed the work after talking to Design, and Branding kept the old design.
- **Procurement and Furniture are Agency now** (Prateek, via Narendra, 6 Nov). They stay on the map only where they touch Build. The PM arranges furniture and stock with Logistics directly.
- **Site status lives in WhatsApp,** and stand lists in one Excel per PM. Nothing joins them.
- **Labour (own and outside) is recorded almost nowhere.** Only Carpentry and Paint have someone hired for it.

Whole company: Agency, the PM as the bridge, and Build

Ravashing Exhibitions & Events · 6 Nov 2026 · Confidential. Build side from our talks. Agency side from Prateek's chart and notes (told, not confirmed) and our guesses. Marketing and HR are dimmed: not studied.

Line style — confirmed · told, not confirmed · assumed — **Colour = channel** — Paper printout · WhatsApp · Email / shared files · Excel / list · Phone / in person · Talk that bypasses the PM

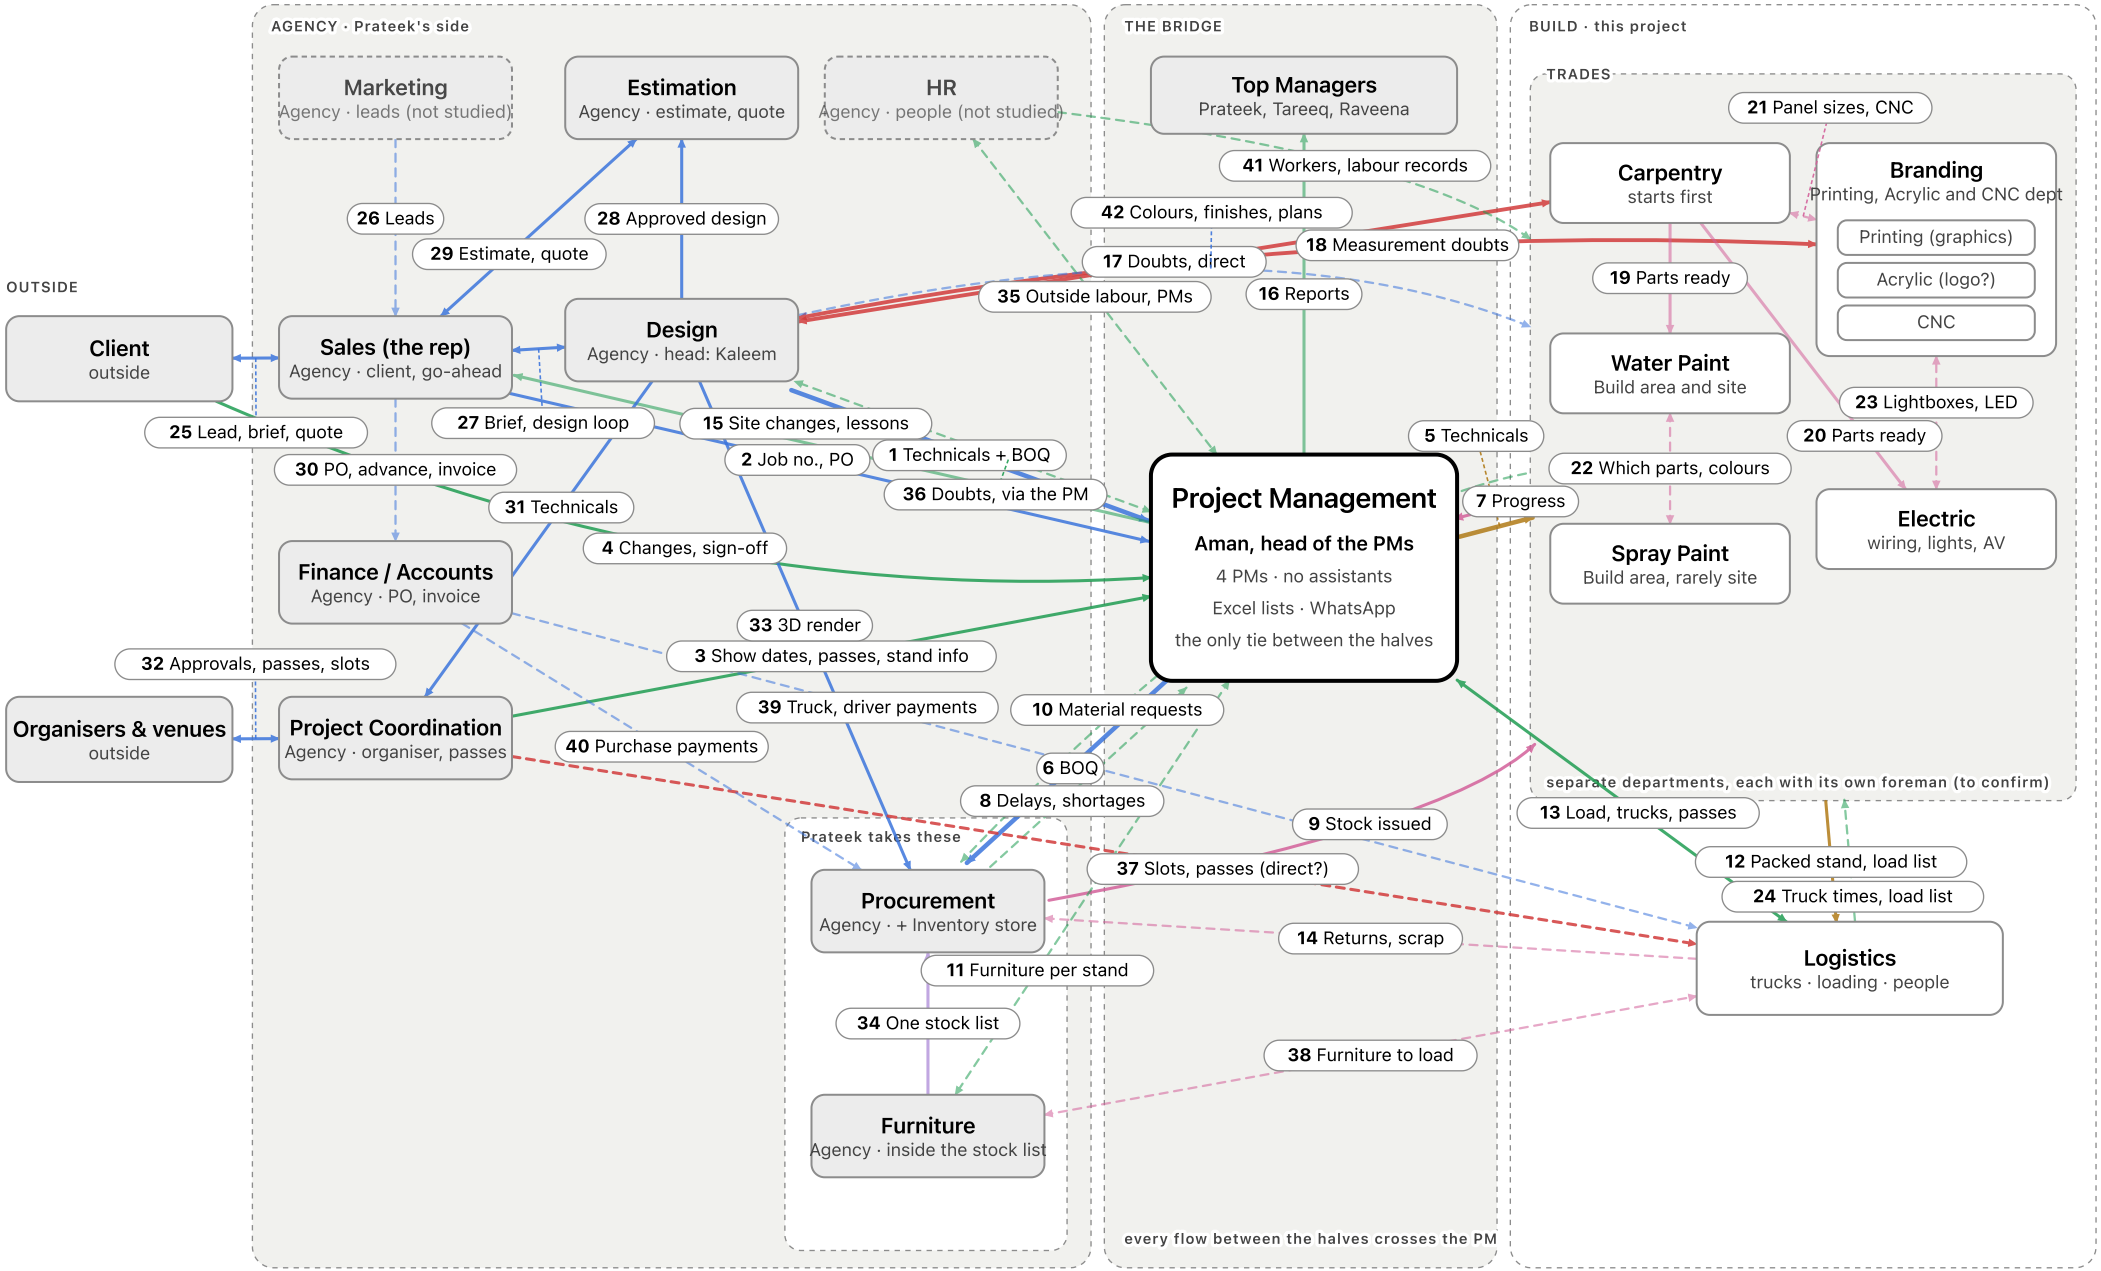

Key to the numbered flows, whole company

● confirmed by someone doing that work ◐ told to us, not yet confirmed ○ our guess from similar companies. A ? after a channel means the channel is a guess. Team sizes are guesses.

#	From	To	Data	Channel	Who reads it on arrival (our guess)	Status
1	Design	Project Management	Technicals (3D design, 2D plan, colour codes, item and AV lists, special elements) and the BOQ	Email / shared files? WhatsApp?	The PM who owns the stand; Aman sees it too	● Confirmed by someone doing that work
2	Sales (the rep)	Project Management	The rep gives the go-ahead to release; PO and advance received, job number opened	Email / shared files? WhatsApp?	The PM who owns the stand; Aman	◐ Told by someone else, not yet confirmed
3	Project Coordination	Project Management	Show dates, build-up windows, passes, organiser approvals, and stand information (the Sales team sends stand information too)	WhatsApp	The PMs on that show; Aman	◐ Told by someone else, not yet confirmed
4	Client	Project Management	Change requests during the build; walk-through and sign-off	WhatsApp	The PM who owns the stand	◐ Told by someone else, not yet confirmed
5	Project Management	the five trades	Printed technicals pack for Carpentry, Water Paint, Spray Paint, Electric and Branding	Paper printout? WhatsApp?	Each trade's foreman, who passes it to the workers	● Confirmed by someone doing that work
6	Project Management	Procurement	BOQ: list of items and quantities (Prateek's note says there is no per-stand BOQ: Procurement reads the 3D render; open)	Email / shared files? Excel / list?	The buyer or store keeper who does the stock check	● Confirmed by someone doing that work
7	the five trades	Project Management	Progress of each stand and people counts per trade; also what goes back up to the PM: build schedule, site dates, client questions	Phone / in person? WhatsApp?	The PM who owns the stand	◐ Told by someone else, not yet confirmed
8	Procurement	Project Management	Missing items and late deliveries	WhatsApp? Phone / in person?	The PM who owns the stand	○ Assumed from similar companies
9	Procurement	the five trades	Items and materials from the store for the five trades	Phone / in person? Paper printout?	The foreman, and the workers who collect from the store	◐ Told by someone else, not yet confirmed
10	the five trades	Procurement	Requests for items not on the BOQ, such as unique client items	WhatsApp? Phone / in person?	The buyer or store keeper	○ Assumed from similar companies
11	Project Management	Furniture (both ways)	Which furniture each stand needs; ready or short (Furniture is Agency side)	WhatsApp? Excel / list?	The furniture coordinator; the PM	○ Assumed from similar companies
12	the five trades	Logistics	Dismantled, labelled stand parts and a signed load list	Paper printout? Phone / in person?	The transport planner or dispatcher; loaders use the load list	◐ Told by someone else, not yet confirmed
13	Project Management	Logistics (both ways)	Ready-to-load signal; furniture and stock to load, also before the site; truck left, reached, offloaded; venue slots and passes handed down from the Coordinators	WhatsApp Phone / in person	The transport planner or dispatcher; the PM	◐ Told by someone else, not yet confirmed

#	From	To	Data	Channel	Who reads it on arrival (our guess)	Status
14	Logistics	Procurement	Items back from the show; scrap	Phone / in person?	The store keeper (Inventory)	○ Assumed from similar companies
15	Project Management	Sales (the rep)	Updates go to Sales and the top managers (told); site changes for the final invoice; lessons learned	WhatsApp? Excel / list?	Accounts (final invoice) and Sales	◐ Told by someone else, not yet confirmed
16	Project Management	Top Managers	Updates to the boss (told, not clear which top manager); progress and status reports	WhatsApp? Excel / list?	Top Managers	◐ Told by someone else, not yet confirmed
17	Design	Carpentry (both ways)	Doubts about a drawing are sometimes answered by Design directly; the PM may not hear about the change	Phone / in person? WhatsApp?	The Carpentry foreman; the designer at Design who answers	◐ Told by someone else, not yet confirmed
18	Design	Branding (both ways)	Questions to Design about measurements, besides the drawings that come from the PM	WhatsApp?	The Branding foreman or designer; Design	◐ Told by someone else, not yet confirmed
19	Carpentry	Water Paint	Some parts are ready, so Paint starts primer	Phone / in person?	The Paint foreman	◐ Told by someone else, not yet confirmed
20	Carpentry	Electric	Some parts are ready, so Electric starts fixing	Phone / in person?	The Electric foreman	◐ Told by someone else, not yet confirmed
21	Carpentry	Branding (both ways)	Sizes the graphics must fit; CNC cut files and cut parts for Carpentry (CNC sits under Branding)	Phone / in person?	The Branding foreman; the Carpentry foreman	○ Assumed from similar companies
22	Water Paint	Spray Paint (both ways)	Which parts are sprayed and which are water-painted; colour codes; order of work on a stand	Phone / in person?	The Water Paint and Spray Paint heads	○ Assumed from similar companies
23	Electric	Branding (both ways)	Cut-outs and power points for lightboxes and LED graphics; sizes	Phone / in person?	The Electric and Branding heads	○ Assumed from similar companies
24	Logistics	the five trades	Truck schedule and loading times to the trades; the trades pack to the load list	WhatsApp? Phone / in person?	Each trade's foreman	○ Assumed from similar companies
25	Client	Sales (the rep) (both ways)	The client talks only to the rep: lead, brief, design changes, quote, negotiation (Prateek's chart and note)	Email / shared files? WhatsApp?	The rep	◐ Told by someone else, not yet confirmed
26	Marketing	Sales (the rep)	Leads reach the rep (our guess; Marketing is not studied yet)	Email / shared files?	The rep	○ Assumed from similar companies
27	Sales (the rep)	Design (both ways)	The rep passes the brief to Design; the client's changes come back through the rep until Design is approved (Prateek's chart)	Email / shared files? Phone / in person?	Design, and the rep	◐ Told by someone else, not yet confirmed
28	Design	Estimation	Once the design is approved, Estimation costs it (Prateek's chart)	Email / shared files?	Estimation	◐ Told by someone else, not yet confirmed
29	Estimation	Sales (the rep) (both ways)	The estimate becomes the quote; a drastic change loops back to Estimation to recost (Prateek's chart)	Email / shared files? Excel / list?	The rep, and Estimation when recosting	◐ Told by someone else, not yet confirmed
30	Sales (the rep)	Finance / Accounts	PO and advance received; final invoice (our guess)	Email / shared files?	Accounts	○ Assumed from similar companies

#	From	To	Data	Channel	Who reads it on arrival (our guess)	Status
31	Design	Project Coordination	Coordination waits for the technicals before it starts (Prateek's chart)	Email / shared files?	Project Coordination	◐ Told by someone else, not yet confirmed
32	Project Coordination	Organisers & venues (both ways)	Organiser and venue approvals, gate passes and venue slots (Prateek's chart)	Email / shared files? WhatsApp?	Project Coordination; the organiser or venue	◐ Told by someone else, not yet confirmed
33	Design	Procurement	Procurement reads the 3D render to split stock, reusable and new to buy (Prateek's note)	Email / shared files?	The buyer or store keeper	◐ Told by someone else, not yet confirmed
34	Furniture	Procurement	Furniture is a category inside Procurement's inventory: one list, one owner (Prateek's note)	Excel / list?	The buyer or store keeper	◐ Told by someone else, not yet confirmed
35	HR	Project Management (both ways)	Aman arranges outside labour and outside PMs; what HR does here is not known	WhatsApp?	Aman; HR	○ Assumed from similar companies
36	Project Management	Design (both ways)	Prateek's rule: every doubt goes to the PM, who takes it to Design. Not yet how it works today	WhatsApp?	The PM; the designer	○ Assumed from similar companies
37	Project Coordination	Logistics	Slots and passes may reach Logistics directly; the rule says through the PM	WhatsApp? Email / shared files?	Logistics	○ Assumed from similar companies
38	Furniture	Logistics (both ways)	Furniture ready to load, and back after the show. The PM coordinates it, before the site too	Phone / in person?	Logistics; the PM	○ Assumed from similar companies
39	Finance / Accounts	Logistics	Payment of hired trucks and drivers (our guess)	Email / shared files?	Accounts	○ Assumed from similar companies
40	Finance / Accounts	Procurement	Payment of orders and vendors (our guess; both are Agency)	Email / shared files?	Accounts; the buyer	○ Assumed from similar companies
41	HR	the five trades	Outside workers and who records their hours: the one hired labour-record person for Carpentry and Paint (our guess for HR's part)	WhatsApp?	The labour-record person; Aman	○ Assumed from similar companies
42	Design	the five trades	Colour codes, finishes, electrical and AV plans. By the rule these go through the PM (our guess for what Design sends)	Email / shared files?	Each trade's foreman	○ Assumed from similar companies

Work flow: who does what, stage by stage

Ravashing Exhibitions & Events, Build side · 6 Nov 2026 · Confidential

● confirmed by someone doing that work ◐ told to us, not yet confirmed ○ our guess from similar companies. A ? after a channel means the channel is a guess. Team sizes are guesses.

	Handoff	Build area: start	Build area: mock-up	Pack & move	On site: build-up	Show & handover	Dismantle & return	Close
Agency	◐ WON. Four tracks start: technicals, coordination, graphics, purchasing (Procurement and Furniture are Agency). The rep gives the go-ahead	◐ Design answers doubts			○ Coordinators: passes, venue rules	◐ Client walk-through and sign-off (Sales + site team)		◐ Accounts: final invoice vs PO and site changes
PM	◐ Collects technicals + BOQ; checks the handover pack; releases to Production	● Hands technicals to trades; Procurement is Agency; tracks progress	● Tracks mock-up; goes to Design for changes	◐ Confirms ready to load; coordinates furniture and stock with Logistics	● Walks stands; tracks steps; WhatsApp status	◐ Handover sheet	○ Tracks what is kept and what is scrapped; passes stock and furniture back through Logistics	◐ Files job, photos, lessons learned
Carpentry		◐ Starts structure: wood, metal, acrylic (CNC is under Branding)	◐ Completes the stand mock-up	◐ Dismantles, labels, load list	◐ Structure, platform (often outside labour)		○ Dismantle; parts back to Build area	
Water Paint		◐ Primer once parts are ready	◐ Water paint		◐ Water paint, putty, sanding, first coat on site			
Spray Paint		○ Spray work once parts are ready	○ Spraying		◐ Rarely on site			
Electric		◐ Small electric fixing once parts are ready	◐ Wiring, lighting, AV fitted and tested		◐ Electric work and fitting		○ Disconnect; equipment back	
Branding		◐ Graphics, CNC and Logo start with Carpentry, from Design's zip file	◐ Prints; mock-up OK'd	○ Prints packed	◐ Logo and graphics fitted			
Logistics				◐ Loads; moves stand, furniture and people; trucks scheduled	◐ Truck reached; offload		○ Return transport; scrap removal	

Site steps a PM tracks, walking from stand to stand

Truck reached → Offloaded → Space identified → Platform work → Electric work → Structure work → Putty → Sanding (?) → Paint first coat → Electric fitting → Logo work

Handoff, from Prateek's chart: after WON four tracks run before release. Technicals (Design: 2D drawings, finishes). Coordination (organisers, venues, approvals, passes; waits for the technicals). Graphics (sizes via the rep, mock-up, print proof). Purchasing (from the 3D render: stock or new to buy). The PM checks the handover pack, the rep gives the go-ahead, and the PM releases to Production.

Steps confirmed by a PM. The order and the full list are not confirmed. "Standing" is assumed to mean sanding. A blank cell means nothing is known yet. Build-area work runs in parallel.

All data flows between departments

Ravashing Exhibitions & Events, Build side · 6 Nov 2026 · Confidential

● confirmed by someone doing that work ◐ told to us, not yet confirmed ○ our guess from similar companies. A ? after a channel means the channel is a guess. Team sizes are guesses.

#	From	To	Data	Channel	Who reads it on arrival (our guess)	Status
1	Design	Project Management	Technicals (3D design, 2D plan, colour codes, item and AV lists, special elements) and the BOQ	Email / shared files? WhatsApp?	The PM who owns the stand; Aman sees it too	● Confirmed by someone doing that work
2	Sales & Accounts	Project Management	The rep gives the go-ahead to release; PO and advance received, job number opened	Email / shared files? WhatsApp?	The PM who owns the stand; Aman	◐ Told by someone else, not yet confirmed
3	Project Coordinators	Project Management	Show dates, build-up windows, passes, organiser approvals, and stand information (the Sales team sends stand information too)	WhatsApp	The PMs on that show; Aman	◐ Told by someone else, not yet confirmed
4	Client	Project Management	Change requests during the build; walk-through and sign-off	WhatsApp	The PM who owns the stand	◐ Told by someone else, not yet confirmed
5	Project Management	the five trades	Printed technicals pack for Carpentry, Water Paint, Spray Paint, Electric and Branding	Paper printout? WhatsApp?	Each trade's foreman, who passes it to the workers	● Confirmed by someone doing that work
6	Project Management	Procurement	BOQ: list of items and quantities (Prateek's note says there is no per-stand BOQ: Procurement reads the 3D render; open)	Email / shared files? Excel / list?	The buyer or store keeper who does the stock check	● Confirmed by someone doing that work
7	the five trades	Project Management	Progress of each stand and people counts per trade; also what goes back up to the PM: build schedule, site dates, client questions	Phone / in person? WhatsApp?	The PM who owns the stand	◐ Told by someone else, not yet confirmed
8	Procurement	Project Management	Missing items and late deliveries	WhatsApp? Phone / in person?	The PM who owns the stand	○ Assumed from similar companies
9	Procurement	the five trades	Items and materials from the store for the five trades	Phone / in person? Paper printout?	The foreman, and the workers who collect from the store	◐ Told by someone else, not yet confirmed
10	the five trades	Procurement	Requests for items not on the BOQ, such as unique client items	WhatsApp? Phone / in person?	The buyer or store keeper	○ Assumed from similar companies
11	Project Management	Furniture (both ways)	Which furniture each stand needs; ready or short (Furniture is Agency side)	WhatsApp? Excel / list?	The furniture coordinator; the PM	○ Assumed from similar companies
12	the five trades	Logistics	Dismantled, labelled stand parts and a signed load list	Paper printout? Phone / in person?	The transport planner or dispatcher; loaders use the load list	◐ Told by someone else, not yet confirmed

#	From	To	Data	Channel	Who reads it on arrival (our guess)	Status
13	Project Management	Logistics (both ways)	Ready-to-load signal; furniture and stock to load, also before the site; truck left, reached, offloaded; venue slots and passes handed down from the Coordinators	WhatsApp; Phone / in person	The transport planner or dispatcher; the PM	◐ Told by someone else, not yet confirmed
14	Logistics	Procurement	Items back from the show; scrap	Phone / in person?	The store keeper (Inventory)	○ Assumed from similar companies
15	Project Management	Sales & Accounts	Updates go to Sales and the top managers (told); site changes for the final invoice; lessons learned	WhatsApp?; Excel / list?	Accounts (final invoice) and Sales	◐ Told by someone else, not yet confirmed
16	Project Management	Top Managers	Updates to the boss (told, not clear which top manager); progress and status reports	WhatsApp?; Excel / list?	Top Managers	◐ Told by someone else, not yet confirmed
17	Design	Carpentry (both ways)	Doubts about a drawing are sometimes answered by Design directly; the PM may not hear about the change	Phone / in person?; WhatsApp?	The Carpentry foreman; the designer at Design who answers	◐ Told by someone else, not yet confirmed
18	Design	Branding (both ways)	Questions to Design about measurements, besides the drawings that come from the PM	WhatsApp?	The Branding foreman or designer; Design	◐ Told by someone else, not yet confirmed
19	Carpentry	Water Paint	Some parts are ready, so Paint starts primer	Phone / in person?	The Paint foreman	◐ Told by someone else, not yet confirmed
20	Carpentry	Electric	Some parts are ready, so Electric starts fixing	Phone / in person?	The Electric foreman	◐ Told by someone else, not yet confirmed
21	Carpentry	Branding (both ways)	Sizes the graphics must fit; CNC cut files and cut parts for Carpentry (CNC sits under Branding)	Phone / in person?	The Branding foreman; the Carpentry foreman	○ Assumed from similar companies
22	Water Paint	Spray Paint (both ways)	Which parts are sprayed and which are water-painted; colour codes; order of work on a stand	Phone / in person?	The Water Paint and Spray Paint heads	○ Assumed from similar companies
23	Electric	Branding (both ways)	Cut-outs and power points for lightboxes and LED graphics; sizes	Phone / in person?	The Electric and Branding heads	○ Assumed from similar companies
24	Logistics	the five trades	Truck schedule and loading times to the trades; the trades pack to the load list	WhatsApp?; Phone / in person?	Each trade's foreman	○ Assumed from similar companies

Questions for each department

Ravashing Exhibitions & Events, Build side · 6 Nov 2026 · Confidential

★ = ask first if you only have ten minutes. The tag says which part of the map the answer fills. Ask about the last real stand, not how things usually go.

Project Management: Ali and other PMs

1. People ★ How many stands does one PM handle at a time, normally and at the most? Who looks after your stands when you are at another show? How many outside PMs do we hire at the busiest time, and who arranges them?

2. Flows ★ What do you receive from Design, Sales and the Coordinators (files, dates, passes)? How does each one reach you? Open one real technicals pack with me: what do you call the BOQ in it, and are colour codes (Pantones) on it? Do you check a handover pack before you release to Production: what is in it, who is the rep who gives the go-ahead, and what happens if something is missing?

3. Flows What exactly do you hand to each trade and to Logistics? How do you arrange furniture and stock with Logistics (before the site too), and how do you pass on the venue slots and passes from the Coordinators? When something changes, how do you tell them? What do you send back to the rep and the client: build schedule, site dates, questions?

4. Records ★ When you update Sales and the boss, who is the boss here, how do you send it (WhatsApp?) and who writes it down? Can you show me your Excel and one WhatsApp group for a stand? What is in each column, who else can see them, and where do the photos go?

5. Work At the Build area, how do you know how far each stand has got? How early can you tell it will be late?

6. Site On site with 10 or 20 stands: how many PMs are there, how do you note each step, and who guides the workers at a stand when you are at another one? How do you brief outside labour or outside PMs?

7. Problem ★ Is it normal for a foreman to talk to Design directly? What would stop the old-design mistake from happening again, without everything having to go through you?

8. Close How does a stand end: handover sheet, sign-off, photos, and what you tell Accounts about site changes? And what one thing do you wish you could see on your phone each morning?

Project Management: Aman, head of PMs

1. People ★ What does Production Coordination (two people between the PMs and the divisions) do, and what do they write down? What can you decide yourself, and what must go to the General Manager or the top managers?

2. Work ★ How do you give a stand to a PM? How do you see all stands and every PM's load today?

3. Capacity ★ When two stands need the same people or machines, who decides? When did you last bring in outside people for work, labour or PMs?

4. Capacity Which outside companies do you use, who keeps the list, who approves and pays, and how many outside people do you have at the busiest time?

5. Flows What do you report to the Top Managers, and how often? What do you need from each department, and when?

6. Problem How do you find out a stand is in trouble? Which shows are coming next month, and how many stands are in each?

Carpentry

1. People ★ The chart shows three senior carpenters under the foreman: who leads what, and which machine does each run? Who gives you your daily work: the PM or Production Coordination? Who does the metal work? How many outside carpenters do we use at the busiest time?

2. Work Take your last stand, from getting the technicals to the mock-up. How did you decide Paint and Electric could start, and who said the mock-up was good?

3. Flows ★ Who gives you the technicals? Last time you had a doubt about a drawing, who did you ask, and did you tell the PM?

4. Flows Which other departments do you talk to (Paint, Spray Paint, Electric, Branding, Logistics) and about what? Phone, WhatsApp, paper or in person?

5. Records ★ What do you write down: progress, materials, who worked, hours? Today the PMs keep your information. What do you tell the PM about progress, and how (phone, WhatsApp)? What would you need if you kept a simple list yourself? Can you show me anything you write down?

6. Capacity How many stands at once is too many? Who decides which goes first, and when do you use outside carpenters? What do your people do on site, and who guides outside workers there?

7. Problem ★ What went wrong most recently, and who noticed first? What one thing do you wish you could see quickly?

Water Paint

1. People ★ Who heads Water Paint, and is there a manager above him? How many people are in the team (ours and outside, normally and at the busiest)? Who keeps the labour information?

2. Work Take your last stand, from the first parts arriving to finished. What do you paint (water paint and primer), and how is it different from spray paint? What is done here, and what is left for site?

3. Flows ★ How do you know a part is ready for you, and where do the colours come from? If the colour changes, how do you hear? Which departments do you talk to, and how?

4. Records ★ What do you write down: paint used, colours, who worked, hours? Who keeps these records, and where? Can you show me?

5. Capacity How many stands at once? Who decides which goes first, and when do you use outside painters? Who paints on site, and who briefs them on colours? How do you work with Spray Paint?

6. Problem ★ What went wrong most recently, and who noticed first? What one thing do you wish you could see quickly?

Electric

1. People ★ Who gives you your daily work: the PM or Production Coordination? Who are the outside AV and lighting people, who books them, and how many do we use at the busiest time? When the six electricians are all busy, who does the extra work?

2. Work What do you fit at the Build area, and what is left for site? Who makes the plan for sockets and lights, and how do you test your work?

3. Flows ★ How do you know a stand is ready for you? If the electrical plan changes, how do you hear? Which departments do you talk to, and how?

4. Records ★ On site, does anyone besides the PM note your progress? Which lights, cables and AV items do we own, reuse or hire, and who tracks where they are? How do you ask Procurement for material?

5. Capacity How many stands at once? Who decides which goes first, and when do you use outside electricians? Who connects to the venue power and tests before opening?

6. Problem ★ What went wrong most recently, and who noticed first? What one thing do you wish you could see quickly?

Spray Paint

1. People ★ Who is the foreman, and is there a manager above him? How many people are in the team (ours and outside, normally and at the busiest)? Why is spray paint a separate department from Paint?

2. Work Take your last stand: when do parts reach you, where do you spray, and how long do they dry? Is the spray area or drying time ever a limit? What makes you spray on site in the rare cases, and who decides?

3. Flows ★ How do you know a part is ready for you, and who gives you the colours? If a colour changes, how do you hear? How do you work with Paint and Carpentry, and who do you tell when you finish?

4. Records ★ What do you write down: paint used, colours, who worked, hours? Who keeps these records, and where? Can you show me?

5. Capacity How many stands at once? Who decides which goes first, and when do you use outside spray painters?

6. Problem ★ What went wrong most recently, and who noticed first? What one thing do you wish you could see quickly?

Branding (Graphics, CNC, Logo)

1. People ★ On the HR chart this department is called Printing, Acrylic and CNC, with no Branding box. Is Branding the same department? Where does Logo fit: is it the acrylic work? How many outside people do we use at the busiest time?

2. Work Take your last stand, from the zip file you get from Design to graphics on the stand. What is in the zip? What do you print yourselves and what goes outside? What are the graphic and logo mock-ups, and who approves them?

3. Flows ★ Who gives you the technicals and the logo? Has the client already approved the sizes and the print proof before you start? Who do you ask about measurements? How do you hear a design changed, and has anything been printed twice?

4. Flows How do you tell the PM your progress, and how do you agree sizes with Carpentry? Which other departments do you talk to, and how?

5. Records ★ Where are the final print files kept, who keeps them, and how do you know which version was printed? What else do you write down?

6. Parts What does each part do: Graphics, CNC, Logo? What does CNC cut, and for whom (Carpentry too)? How does a finished logo reach the stand?

7. Site Who fits the graphics on site? What happens if one does not fit? How many stands at once, and when do you use outside people?

8. Problem ★ What went wrong most recently, and who noticed first? What one thing do you wish you could see quickly?

Logistics

1. People ★ The chart shows Transport as 7 people. Does Transport do only trucks and loading, or also site work? Who plans the trucks and keeps the bookings? Are the vehicles ours or hired, and who do you take work from: the PM or Production Coordination?

2. Work Take the last stand you sent. How did you know it was ready, who made the load list, and who checked it at the site?

3. Flows ★ Do you get venue slots and passes from the PM or from the Coordinators? How do the PM and you arrange furniture and stock to load? How does the PM learn the truck has left, reached and offloaded? Which other departments do you talk to?

4. Records ★ What do you write down: bookings, load lists, costs for each stand? Who writes it, and where? Is there one place where all coming site dates can be seen?

5. After Does your work stop at delivery, or do you help build? Who is in charge at site? After the show, what comes back, who checks it, and who removes the scrap and at what cost?

6. Overseas For jobs outside the UAE, how does the stand get there? Who handles shipping and customs, and who travels?

7. Problem ★ How many stands do you move in the same week, and who decides which goes first? What went wrong most recently?

Prateek

Structure, the edge with Agency, money and limits. ★ = ask first.

Name and role: _____ Date: _____

QUESTIONS

1. People ★ Your seam note says Procurement lives on both sides, and the HR chart puts the Furniture division inside Production, but we were told Procurement and Furniture are Agency. Which is right for each? Is Branding the Printing, Acrylic and CNC department?

2. People ★ What does each top manager look at? When PMs update the boss, who is that? Who settles it when department heads disagree?

3. Flows ★ What is in the handover pack today, who builds it, and in what form? Your clash note says there is no BOQ per stand and no colour codes on the drawings, but our PMs say both arrive. Can we open one real technicals pack together?

4. Flows ★ After release, how should a design change reach Build? What are the DMS and the Build Spec, and when will they exist? Who raises a change order? What must Build send back (schedule, site dates, client questions), and to whom?

5. Edge ★ When will Stand Studio be live? If it is late, can Build start with stands typed in by hand?

6. Edge ★ Which side of the dashed line is the PM: RAVS or Build? What do RAVS and AI engineer stand for? Who agreed that your map wins up to release, and may Build add to the handover pack?

7. Money Who in Build may see prices? Does anyone compare planned and actual cost? Which accounting software does Accounts use?

8. Outside How often do we use outside companies, which ones, and who keeps the list? Would outside people ever use our system? Who builds our stands overseas?

9. Limits ★ What would success look like, and by when? Can I have the approved tools list (Annex A), any data rules, the budget for phones and Wi-Fi, and the name of my backup person?
