
Map: how work and data move between departments

Ravashing Exhibitions & Events, Build side · 6 Nov 2026 · Confidential

Line style — confirmed · told, not confirmed · assumed

Colour = channel — Paper printout · WhatsApp · Email / shared files · Excel / list · Phone / in person · Talk that bypasses the PM

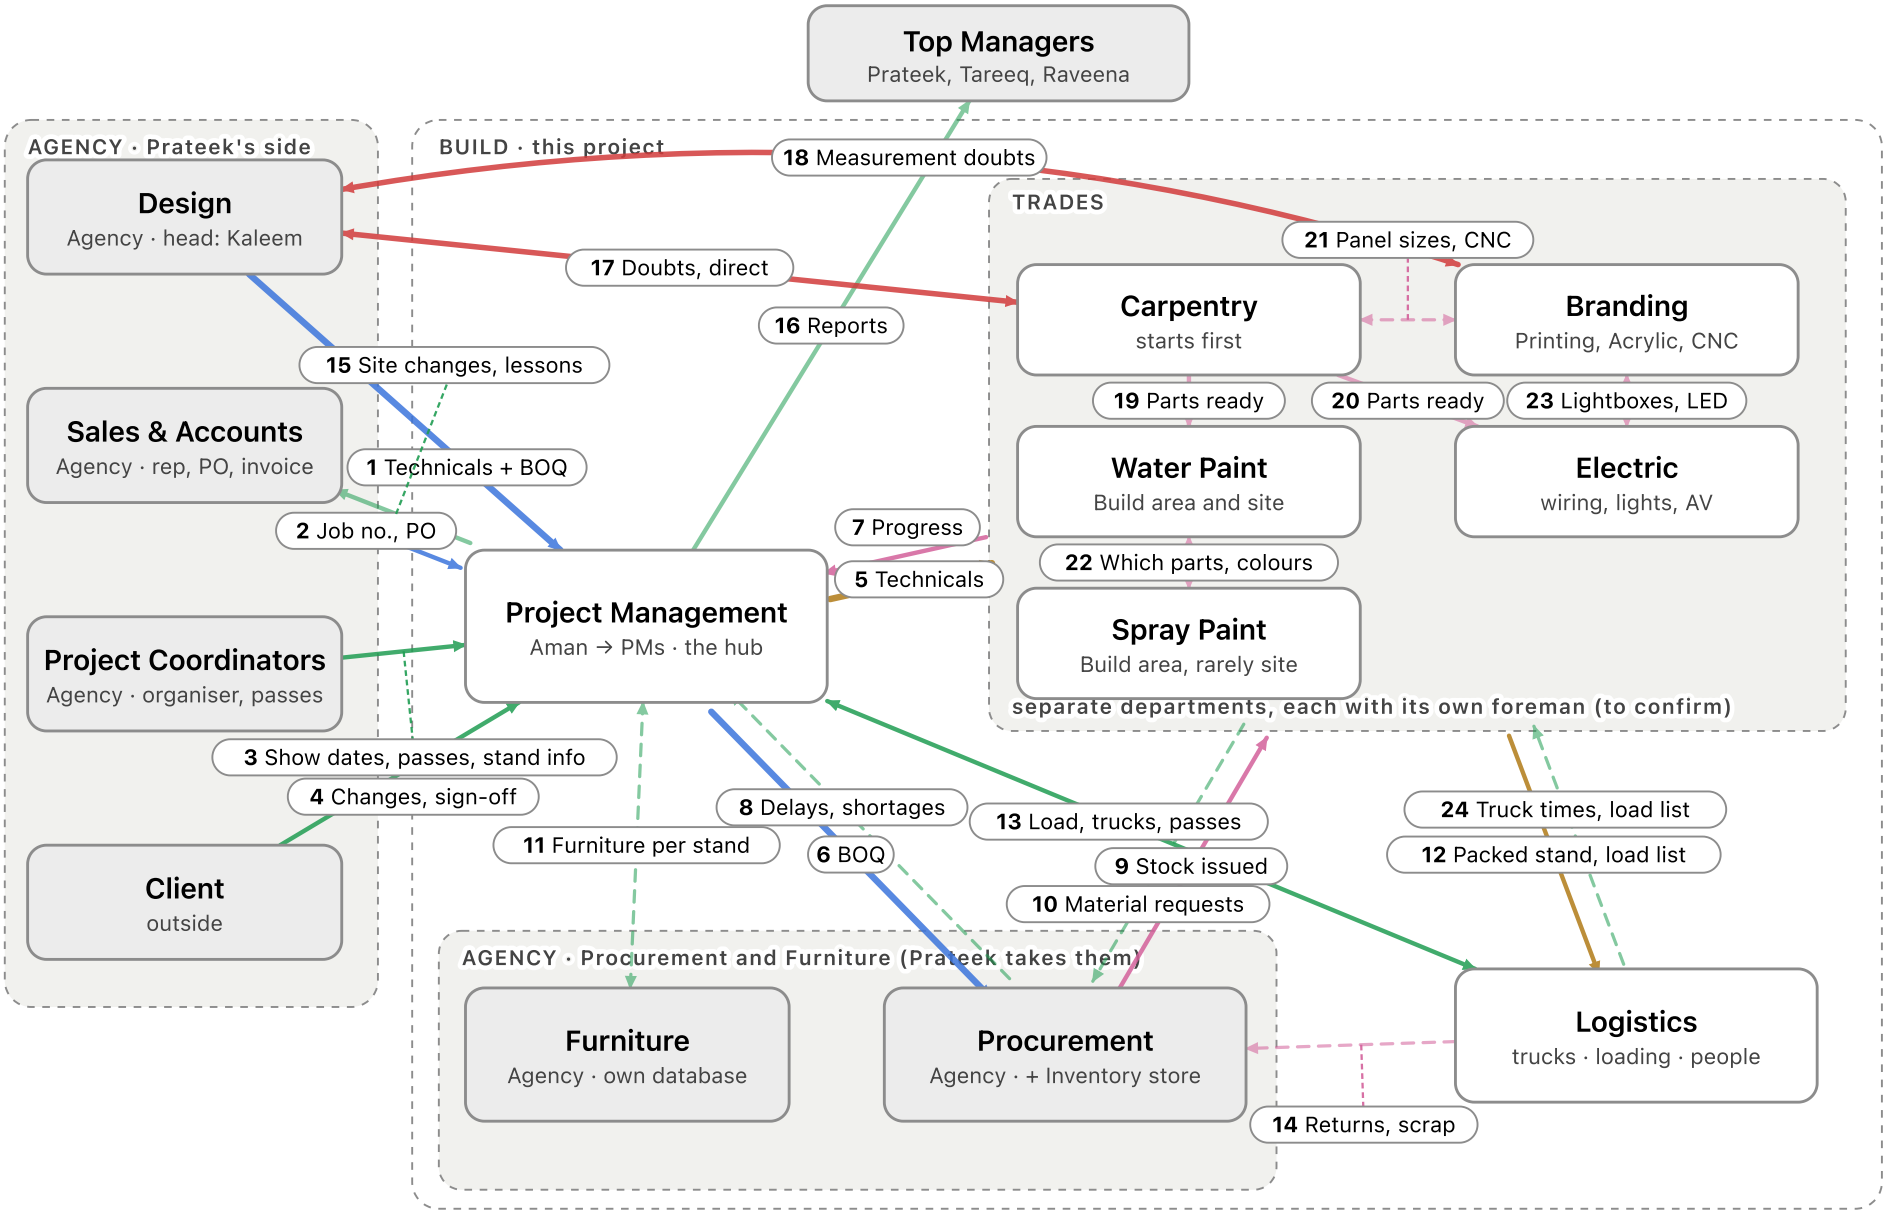

Key to the numbered flows

● confirmed by someone doing that work ◐ told to us, not yet confirmed ○ our guess from similar companies. A ? after a channel means the channel is a guess. Team sizes are guesses.

#	From	To	Data	Channel	Who reads it on arrival (our guess)	Status
1	Design	Project Management	Technicals (3D design, 2D plan, colour codes, item and AV lists, special elements) and the BOQ	Email / shared files? WhatsApp?	The PM who owns the stand; Aman sees it too	● Confirmed by someone doing that work
2	Sales & Accounts	Project Management	The rep gives the go-ahead to release; PO and advance received, job number opened	Email / shared files? WhatsApp?	The PM who owns the stand; Aman	◐ Told by someone else, not yet confirmed
3	Project Coordinators	Project Management	Show dates, build-up windows, passes, organiser approvals, and stand information (the Sales team sends stand information too)	WhatsApp	The PMs on that show; Aman	◐ Told by someone else, not yet confirmed
4	Client	Project Management	Change requests during the build; walk-through and sign-off	WhatsApp	The PM who owns the stand	◐ Told by someone else, not yet confirmed
5	Project Management	the five trades	Printed technicals pack for Carpentry, Water Paint, Spray Paint, Electric and Branding	Paper printout? WhatsApp?	Each trade's foreman, who passes it to the workers	● Confirmed by someone doing that work
6	Project Management	Procurement	BOQ: list of items and quantities (Prateek's note says there is no per-stand BOQ: Procurement reads the 3D render; open)	Email / shared files? Excel / list?	The buyer or store keeper who does the stock check	● Confirmed by someone doing that work
7	the five trades	Project Management	Progress of each stand and people counts per trade; also what goes back up to the PM: build schedule, site dates, client questions	Phone / in person? WhatsApp?	The PM who owns the stand	◐ Told by someone else, not yet confirmed
8	Procurement	Project Management	Missing items and late deliveries	WhatsApp? Phone / in person?	The PM who owns the stand	○ Assumed from similar companies
9	Procurement	the five trades	Items and materials from the store for the five trades	Phone / in person? Paper printout?	The foreman, and the workers who collect from the store	◐ Told by someone else, not yet confirmed
10	the five trades	Procurement	Requests for items not on the BOQ, such as unique client items	WhatsApp? Phone / in person?	The buyer or store keeper	○ Assumed from similar companies
11	Project Management	Furniture (both ways)	Which furniture each stand needs; ready or short (Furniture is Agency side)	WhatsApp? Excel / list?	The furniture coordinator; the PM	○ Assumed from similar companies
12	the five trades	Logistics	Dismantled, labelled stand parts and a signed load list	Paper printout? Phone / in person?	The transport planner or dispatcher; loaders use the load list	◐ Told by someone else, not yet confirmed
13	Project Management	Logistics (both ways)	Ready-to-load signal; furniture and stock to load, also before the site; truck left, reached, offloaded; venue slots and passes handed down from the Coordinators	WhatsApp Phone / in person	The transport planner or dispatcher; the PM	◐ Told by someone else, not yet confirmed

#	From	To	Data	Channel	Who reads it on arrival (our guess)	Status
14	Logistics	Procurement	Items back from the show; scrap	Phone / in person?	The store keeper (Inventory)	○ Assumed from similar companies
15	Project Management	Sales & Accounts	Updates go to Sales and the top managers (told); site changes for the final invoice; lessons learned	WhatsApp? Excel / list?	Accounts (final invoice) and Sales	◐ Told by someone else, not yet confirmed
16	Project Management	Top Managers	Updates to the boss (told, not clear which top manager); progress and status reports	WhatsApp? Excel / list?	Top Managers	◐ Told by someone else, not yet confirmed
17	Design	Carpentry (both ways)	Doubts about a drawing are sometimes answered by Design directly; the PM may not hear about the change	Phone / in person? WhatsApp?	The Carpentry foreman; the designer at Design who answers	◐ Told by someone else, not yet confirmed
18	Design	Branding (both ways)	Questions to Design about measurements, besides the drawings that come from the PM	WhatsApp?	The Branding foreman or designer; Design	◐ Told by someone else, not yet confirmed
19	Carpentry	Water Paint	Some parts are ready, so Paint starts primer	Phone / in person?	The Paint foreman	◐ Told by someone else, not yet confirmed
20	Carpentry	Electric	Some parts are ready, so Electric starts fixing	Phone / in person?	The Electric foreman	◐ Told by someone else, not yet confirmed
21	Carpentry	Branding (both ways)	Sizes the graphics must fit; CNC cut files and cut parts for Carpentry (CNC sits under Branding)	Phone / in person?	The Branding foreman; the Carpentry foreman	○ Assumed from similar companies
22	Water Paint	Spray Paint (both ways)	Which parts are sprayed and which are water-painted; colour codes; order of work on a stand	Phone / in person?	The Water Paint and Spray Paint heads	○ Assumed from similar companies
23	Electric	Branding (both ways)	Cut-outs and power points for lightboxes and LED graphics; sizes	Phone / in person?	The Electric and Branding heads	○ Assumed from similar companies
24	Logistics	the five trades	Truck schedule and loading times to the trades; the trades pack to the load list	WhatsApp? Phone / in person?	Each trade's foreman	○ Assumed from similar companies

Details by department

● confirmed by someone doing that work ◐ told to us, not yet confirmed ○ our guess from similar companies. A ? after a channel means the channel is a guess. Team sizes are guesses.

Flow numbers (#) match the map. The key on the previous pages gives the full wording, the channel, who reads it and the status.

Project Management

Hub between Agency and Build: everything crosses through the PM (Prateek). Four PMs plus Aman; no assistants; no standard Excel list. Each PM owns individual stands; Aman allocates them and arranges outside help. Runs the site. Also coordinates furniture and inventory with Logistics, before the site too.

Team size (our guess): Aman plus 3 PMs (HR chart, 6 Nov); outside PMs at peak, number unknown

PEOPLE AND HIERARCHY

- ◐ Top Managers, 3 people (see both halves)
  - ● General Manager above Production
    - ● Aman, head manager of the PMs: allocates stands, arranges outside help
      - ● Project Managers: 3 listed with Aman, each owns stands
      - ● Production Coordination, 2 people, between the PMs and the divisions: role not known
- ◐ No assistants for PMs (told)
- ◐ Outside PMs hired at peak times, number unknown

DATA MANAGER: WHO KEEPS THE RECORDS

● Each PM keeps their own stand list in Excel; there is no standard list (told)

○ Aman probably collects an overview

NEEDS (RECEIVES)

#1 ● **Design**: Technicals + BOQ

#2 ◐ **Sales & Accounts**: Job no., PO

#3 ◐ **Project Coordinators**: Show dates, passes, stand info

#4 ◐ **Client**: Changes, sign-off

#7 ◐ **the five trades**: Progress

#8 ○ **Procurement**: Delays, shortages

#11 ○ **Furniture**: Furniture per stand

#13 ◐ **Logistics**: Load, trucks, passes

CREATES

● Stand list, one Excel per PM

● Site status updates (WhatsApp)

◐ Printed technicals pack for each trade

◐ Handover sheet

◐ Job file, photos, lessons learned

PASSES ON (SENDS)

#5 ● **the five trades**: Technicals

#6 ● **Procurement**: BOQ

#11 ○ **Furniture**: Furniture per stand

#13 ◐ **Logistics**: Load, trucks, passes

#15 ◐ **Sales & Accounts**: Site changes, lessons

#16 ◐ **Top Managers**: Reports

KEEPS RECORDS IN

● Excel stand lists, one per PM

● WhatsApp groups for stands and for site

◐ Printouts of technicals

Carpentry

Starts first, together with Branding. Builds the structure and the stand mock-up at the Build area. Foremen rarely go to site. Keeps no data of its own: the PMs keep it (told, 6 Nov).

Team size (our guess): 1 foreman plus 24 (HR chart)

PEOPLE AND HIERARCHY

- ● Foreman, 1: head of Carpentry
  - ● Three senior carpenters; one runs a machine
    - ● Carpenters, 21
- ◐ Outside carpentry labour at peak, number unknown
- ◐ Labour-record person, 1, shared with Water Paint
- ● Above the foreman: Production Coordination and Aman

DATA MANAGER: WHO KEEPS THE RECORDS

◐ Nobody in Carpentry: the PMs keep the information (told). The labour-record person keeps labour information

NEEDS (RECEIVES)

#5 ● **Project Management**: Technicals
#9 ◐ **Procurement**: Stock issued
#17 ◐ **Design**: Doubts, direct
#21 ○ **Branding**: Panel sizes, CNC
#24 ○ **Logistics**: Truck times, load list

CREATES

◐ Structure parts
◐ Stand mock-up
◐ Load list (with Logistics)
◐ Progress updates

PASSES ON (SENDS)

#7 ◐ **Project Management**: Progress
#10 ○ **Procurement**: Material requests
#12 ◐ **Logistics**: Packed stand, load list
#17 ◐ **Design**: Doubts, direct
#19 ◐ **Water Paint**: Parts ready
#20 ◐ **Electric**: Parts ready
#21 ○ **Branding**: Panel sizes, CNC

KEEPS RECORDS IN

◐ Labour information, partly (one person hired)
○ Job or cut lists
○ WhatsApp groups

Water Paint

Water Paint department: water paint and primer once parts are ready, at the Build area and on site too. Spray Paint is a separate department.

Team size (our guess): 9 water painters (HR chart); no head named

PEOPLE AND HIERARCHY

- ○ Head of Water Painter: not named on the HR chart
  - ● Water painters, 9
- ○ Outside painters, ≈ 4–15 at peak (guess)
- ◐ Labour-record person, 1, shared with Carpentry
- ● Above: Production Coordination and Aman

DATA MANAGER: WHO KEEPS THE RECORDS

◐ The same labour-record person keeps labour information
○ Water Paint: nobody else known

NEEDS (RECEIVES)

#5 ● **Project Management**: Technicals
#9 ◐ **Procurement**: Stock issued
#19 ◐ **Carpentry**: Parts ready
#22 ○ **Spray Paint**: Which parts, colours
#24 ○ **Logistics**: Truck times, load list

CREATES

◐ Primed and painted parts
◐ Progress updates
○ Paint usage record

PASSES ON (SENDS)

#7 ◐ **Project Management**: Progress
#10 ○ **Procurement**: Material requests
#12 ◐ **Logistics**: Packed stand, load list
#22 ○ **Spray Paint**: Which parts, colours

KEEPS RECORDS IN

◐ Labour information (shared person with Carpentry)
◐ Colour codes, from the technicals

Spray Paint

Separate department from Water Paint. Mostly at the Build area, rarely on site.

Team size (our guess): 3 including the head (HR chart)

PEOPLE AND HIERARCHY

- ● Head of Spray Painter, 1
  - ● Spray painters, 2
- ○ Outside spray painters at peak (not known)
- ● Above: Production Coordination and Aman

DATA MANAGER: WHO KEEPS THE RECORDS

○ The foreman keeps colours, spray schedule and progress notes

NEEDS (RECEIVES)

#5 ● **Project Management**: Technicals
#9 ◐ **Procurement**: Stock issued
#22 ○ **Water Paint**: Which parts, colours
#24 ○ **Logistics**: Truck times, load list

CREATES

○ Sprayed parts
○ Progress updates

PASSES ON (SENDS)

#7 ◐ **Project Management**: Progress
#10 ○ **Procurement**: Material requests
#12 ◐ **Logistics**: Packed stand, load list
#22 ○ **Water Paint**: Which parts, colours

KEEPS RECORDS IN

○ Colour codes, from the technicals
○ Spray area schedule

Electric

Joins once parts are ready. Small electric fixing at the Build area, with no progress update; progress is tracked on site, by the PMs. AV and lighting are outsourced. Orders material from Procurement (told).

Team size (our guess): 7 including the foreman (HR chart); AV and lighting outsourced

PEOPLE AND HIERARCHY

- ● Foreman, 1: head of Electric
  - ● Senior electrician, 1
    - ● Electricians, 5
- ◐ AV and lighting technicians: completely outsourced (told)
- ◐ No helpers (told)
- ● Above: Production Coordination and Aman

DATA MANAGER: WHO KEEPS THE RECORDS

◐ Nobody: the PMs track on-site progress. There is no progress update from the Build area (told)

NEEDS (RECEIVES)

#5 ● **Project Management**: Technicals
#9 ◐ **Procurement**: Stock issued
#20 ◐ **Carpentry**: Parts ready
#23 ○ **Branding**: Lightboxes, LED
#24 ○ **Logistics**: Truck times, load list

CREATES

◐ Wired, lit, tested stand
◐ Progress updates
○ Test record

PASSES ON (SENDS)

#7 ◐ **Project Management**: Progress
#10 ○ **Procurement**: Material requests
#12 ◐ **Logistics**: Packed stand, load list
#23 ○ **Branding**: Lightboxes, LED

KEEPS RECORDS IN

○ Electrical list and plan
○ Equipment (lights, cables) record

Branding

Branding department with three sub-departments: Graphics, CNC and Logo. Gets a zip file from Design. Makes prints and fits graphics on site. Who does the graphic mock-up and print proof is open: Prateek's note puts them with Design (Agency), the print itself with Build.

Team size (our guess): 5 plus the head: Printing 3, Acrylic 1, CNC 1 (HR chart)

PEOPLE AND HIERARCHY

- ● Head of Printing, Acrylic and CNC: sits under the General Manager
  - ● Printing (graphics), 3
  - ● Acrylic, 1
  - ● CNC, 1
- ○ Logo: not on the HR chart; assumed to be acrylic work
- ○ Outside graphic labour at peak, number unknown

DATA MANAGER: WHO KEEPS THE RECORDS

○ The head of Branding, or the designer / prepress person, keeps print files and print orders

NEEDS (RECEIVES)

#5 ● **Project Management**: Technicals
#9 ◐ **Procurement**: Stock issued
#18 ◐ **Design**: Measurement doubts
#21 ○ **Carpentry**: Panel sizes, CNC
#23 ○ **Electric**: Lightboxes, LED
#24 ○ **Logistics**: Truck times, load list

CREATES

◐ Graphic mock-up and logo mock-up
◐ Printed panels, banners, stickers, lightbox fabric
○ Print files

PASSES ON (SENDS)

#7 ◐ **Project Management**: Progress
#10 ○ **Procurement**: Material requests
#12 ◐ **Logistics**: Packed stand, load list
#18 ◐ **Design**: Measurement doubts
#21 ○ **Carpentry**: Panel sizes, CNC
#23 ○ **Electric**: Lightboxes, LED

KEEPS RECORDS IN

○ Print files and versions
◐ Status for the PM

Logistics

Comes in when every department is ready. Loads, moves stands to the event, and moves people. Not yet confirmed as a team of its own.

Team size (our guess): 7 including the head, Transport (HR chart); hired trucks at peak (guess)

PEOPLE AND HIERARCHY

- ● Head of Transport
  - ● Drivers and loaders, 6
- ○ Who plans the trucks? (to find out)
- ○ Hired trucks and drivers, at peak
- ○ Freight agents for overseas jobs
- ● Above: Production Coordination and Aman

DATA MANAGER: WHO KEEPS THE RECORDS

○ The transport planner / dispatcher keeps bookings, load lists and delivery notes

NEEDS (RECEIVES)

#12 ◐ **the five trades**: Packed stand, load list
#13 ◐ **Project Management**: Load, trucks, passes

CREATES

◐ Truck schedule
◐ Load list (with Carpentry)
○ Delivery notes
○ Transport and return records

PASSES ON (SENDS)

#13 ◐ **Project Management**: Load, trucks, passes
#14 ○ **Procurement**: Returns, scrap
#24 ○ **the five trades**: Truck times, load list

KEEPS RECORDS IN

○ Truck bookings
○ Driver and vehicle records

Design

Agency. Releases technicals and answers doubts. Head designer: Kaleem, who OKs graphic mock-ups. Prateek's note: the graphic mock-up and print proof are agency work under the Head of Design.

NEEDS (RECEIVES)

#17 ◐ **Carpentry**: Doubts, direct
#18 ◐ **Branding**: Measurement doubts

PASSES ON (SENDS)

#1 ● **Project Management**: Technicals + BOQ
#17 ◐ **Carpentry**: Doubts, direct
#18 ◐ **Branding**: Measurement doubts

Sales & Accounts

Agency. The rep (sales) owns the client and gives the go-ahead to release the build. Opens the job number, receives the PO and advance, issues the final invoice against site changes.

NEEDS (RECEIVES)

#15 ◐ **Project Management**: Site changes, lessons

PASSES ON (SENDS)

#2 ◐ **Project Management**: Job no., PO

Project Coordinators

Agency. Handle organiser and venue approvals and passes. Build depends on their dates.

NEEDS (RECEIVES)

Nothing known yet.

PASSES ON (SENDS)

#3 ◐ **Project Management**: Show dates, passes, stand info

Client

Outside. Asks for changes, signs off at handover. Often in a WhatsApp group with Sales and the PM.

NEEDS (RECEIVES)

Nothing known yet.

PASSES ON (SENDS)

#4 ◐ **Project Management**: Changes, sign-off

Top Managers

Three people: Prateek, Tareeq and Raveena (Prateek via Narendra, 6 Nov). They see both Agency and Build. What they look at is unknown (ask Prateek).

NEEDS (RECEIVES)

#16 ◐ **Project Management**: Reports

PASSES ON (SENDS)

Nothing known yet.

Notes for Narendra only

Take this page out before showing the map to anyone else.

- **Design doubts bypass the PM.** Red lines show talks that skip the PM. In the case Ali described, Carpentry changed the work after talking to Design, and Branding kept the old design.
- **Procurement and Furniture are Agency now** (Prateek, via Narendra, 6 Nov). They stay on the map only where they touch Build. The PM arranges furniture and stock with Logistics directly.
- **Site status lives in WhatsApp,** and stand lists in one Excel per PM. Nothing joins them.
- **Labour (own and outside) is recorded almost nowhere.** Only Carpentry and Paint have someone hired for it.
