Ravashing: Pain Points and Clashes, Agency vs Build

Nov 6, 2026 · @Prateek


How to read this

Two maps were drawn separately: the agency map from Prateek (lead to Release to Production) and the build-side map from operations (24 numbered flows, a stage-by-stage work flow, and a department-by-department detail). This document lays them against each other and lists only two things: where they contradict each other (a clash), and where either side is already hurting (a pain point). The two halves stay two systems; nothing here merges them.

How sure the build map is matters. Of its 24 flows, 3 are confirmed by someone doing the work (#1, #5, #6), 12 were told second-hand, and 9 are guesses from similar companies. Team sizes and most channels are guesses. So a clash with a guessed flow may just be a wrong guess; a clash with a confirmed flow is a real difference in how the two sides see the work. Each clash below says which it is.

Ruling, agreed 6 Nov 2026: where the two maps disagree on anything up to Release to Production or on the four joints, the agency map rules. Inside the build, the build map rules.

Where the clashes sit

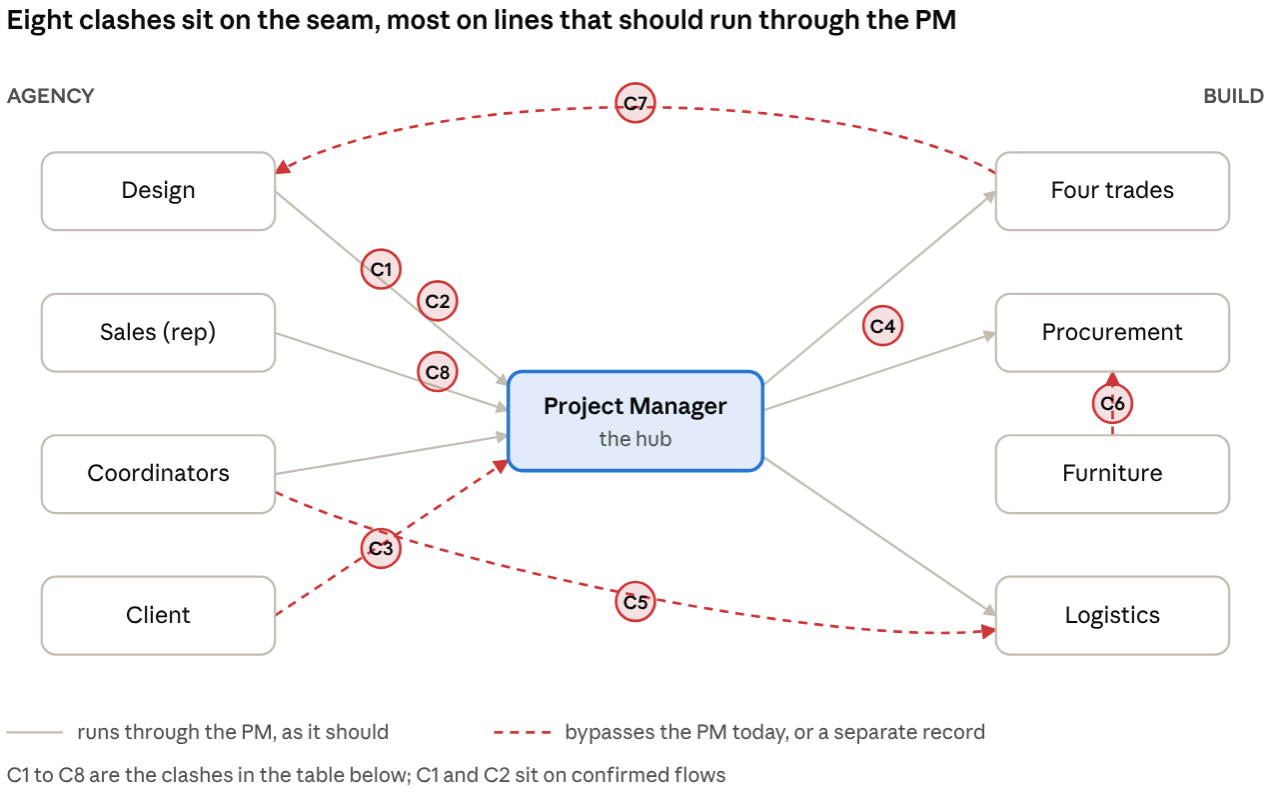

clashes on the seam · 4 bypass lines, 8 clash points

The solid lines are the seam working as both sides want it. The dashed lines are what the build map says happens today and the agency map says should not: the client reaching the PM, coordinators reaching logistics, trades reaching design, and a furniture record living apart from the stock list. C1, C2 and C8 are not bypass lines but arguments about what the handover actually contains.

The clashes

Eight places where the two maps describe the same thing differently. Sureness is the build map's own marker for that flow.

#	Build map says (flow, sureness)	Agency map says	Ruling	Fix
C1	Design sends a BOQ with the technicals (#1, confirmed); PM sends a BOQ to Procurement (#6, confirmed)	There is no per-stand BOQ; Purchasing reads the 3D render	Agency	What the build side calls "the BOQ" is probably the item and AV list inside the technicals. Name it that. Purchasing's own list comes from the render, not from Design
C2	Technicals carry colour codes (#1, confirmed)	Colours are not on the drawings; Pantones are chased from the client mid-build	Agency	The Build Spec in the DMS: one line per coloured element, Pantone or "match to render", finish type. Required before release
C3	Client sends changes and sign-off straight to the PM, often in a WhatsApp group with Sales and the PM (#4, told)	The client talks only to the rep	Agency	The rep stays the client's only contact. Changes during the build are logged by the rep as a change order; the PM reads them, never receives them
C4	Graphics trade makes the graphic and logo mock-ups; Kaleem OKs them (Graphics detail, told)	Head of Design makes the graphic mockup on the confirmed render and sends it for print proof	Agency	Two different things with one name. The design mockup is agency work. The print mock-up is the Graphics trade checking the proof fits the panels. Call them design mockup and print proof

#	Build map says (flow, sureness)	Agency map says	Ruling	Fix
C5	Coordinators send venue slots and passes straight to Logistics (#16, assumed)	All coordination goes to the PM	Agency	Coordinators to PM, PM to Logistics. Redraw #16
C6	Furniture is its own department with its own database; Procurement reads it (#11, told; #12, #14, assumed)	Procurement owns the stock list	Agency	Furniture is a category inside Procurement's inventory. One stock list, one owner. Whether Furniture stays a separate team is operations' call; the data is not separate
C7	Design answers Carpentry and Graphics doubts directly; the PM may not hear (#20, #21, told; the Ali case)	Trades never call the designer; questions go through the PM	Both agree it is a leak	Every doubt goes to the PM, who takes it to Design. The answer is written back on the Build Spec so Graphics and Carpentry read the same change
C8	PM sends site changes to Accounts for the final invoice, and lessons learned to Sales (#18, told)	Nothing. The agency map ends at release and has no change order or final invoice step	Gap on the agency side	Add a change-order record on the agency side, raised by the rep (C3), priced by Estimation when drastic, and summed into the final invoice. Lessons go to Design through the PM

C1 and C2 are the serious ones because the build side marked them confirmed: the people doing the work believe a BOQ and colour codes arrive, and the agency side says they do not. That gap is exactly where the mid-build phone calls come from.

Pain points that are not clashes

Things one side already knows hurt, where the other side has no opinion.

Where	Pain point	Evidence	Who owns the fix
Seam	The handover arrives in pieces: technicals by email, PO by email, dates by WhatsApp, client changes by WhatsApp (#1 to #4). Nothing says "released"	Build map flows 1 to 4, four channels	Agency: Release to Production as one timestamped gate
Seam	Technicals reach the trades as a paper printout (#5, confirmed). A change after release does not reach the paper	Build map #5; the Ali case	Build, after the agency fixes C7: one current version per stand, read from the system, not printed
Seam	The rep's go-ahead to release is a message, not a record (#2)	Build map #2	Agency: the go-ahead is the rep's login pressing a button
Build	Site status lives in WhatsApp; each PM keeps a separate Excel stand list. Nothing joins them	Operations' own notes page	Build
Build	Labour, own and outside, is recorded almost nowhere. Only Carpentry and Paint share one hired record-keeper	Operations' own notes page	Build
Build	Progress from the trades comes by phone or in person (#7, told); delays and shortages the same (#8, assumed)	Build map #7, #8	Build
Build	Nobody is sure who manages above the four foremen, or above Procurement, Furniture and Logistics	"Manager above? to find out" on five department cards	Operations to confirm with Prateek

Where	Pain point	Evidence	Who owns the fix
Agency	The agency map has no step after release for change orders, site sign-off or final invoice (see C8)	Build map #4, #18	Agency
Agency	What Top Management actually looks at is unknown to the build side (#19, assumed)	Build map Top Managers card	Prateek to answer
Both	Lessons from site go to Sales on the build map and to nobody on the agency map. Neither side closes the loop to Design	Build map #18; agency workflow doc	Both, through the PM

What to confirm first

Nine of the build map's flows are guesses. Five of them sit on or next to the seam, so they decide whether a clash above is real. Confirm these with the person who does the work before anything is built on them.

- [ ] #3 Coordinators to PM: show dates, build-up windows, passes. Who actually receives them today, and how?
- [ ] #16 Coordinators to Logistics direct. Does this happen, or does it already go through the PM? Decides C5
- [ ] #12 PM to Furniture: furniture per stand. Who picks the furniture for a stand, and from which list? Decides C6
- [ ] #8 Procurement to PM: delays and shortages. Does the PM hear about a shortage before the trade does?
- [ ] #10 Trades to Procurement: requests for items not on the list. How often, and who approves the spend?

And two confirmed flows that the agency side disputes, which need one sit-down each:

- [ ] #1 and #6, the BOQ. Open a real technicals pack together and point at the thing each side calls the BOQ. Decides C1
- [ ] #1, colour codes. Open the same pack and check whether Pantones are on it. Decides C2
