Ravashing: The Seam Between Agency and Build


Nov 6, 2026 · @Prateek

Two halves, two systems, one seam

Ravashing runs as two businesses in one building: an agency that wins and designs the project, and a stand contractor that builds it. Each half keeps its own map and its own system. They are not merged. They touch at one seam, and almost everything that crosses it goes through the project manager.

The agency map is the Ravashing Agency Workflow Map (Prateek). The build map is the department-flow map (operations). This document records only what joins them, so both maps can change on their own side without breaking the other.

What crosses the seam

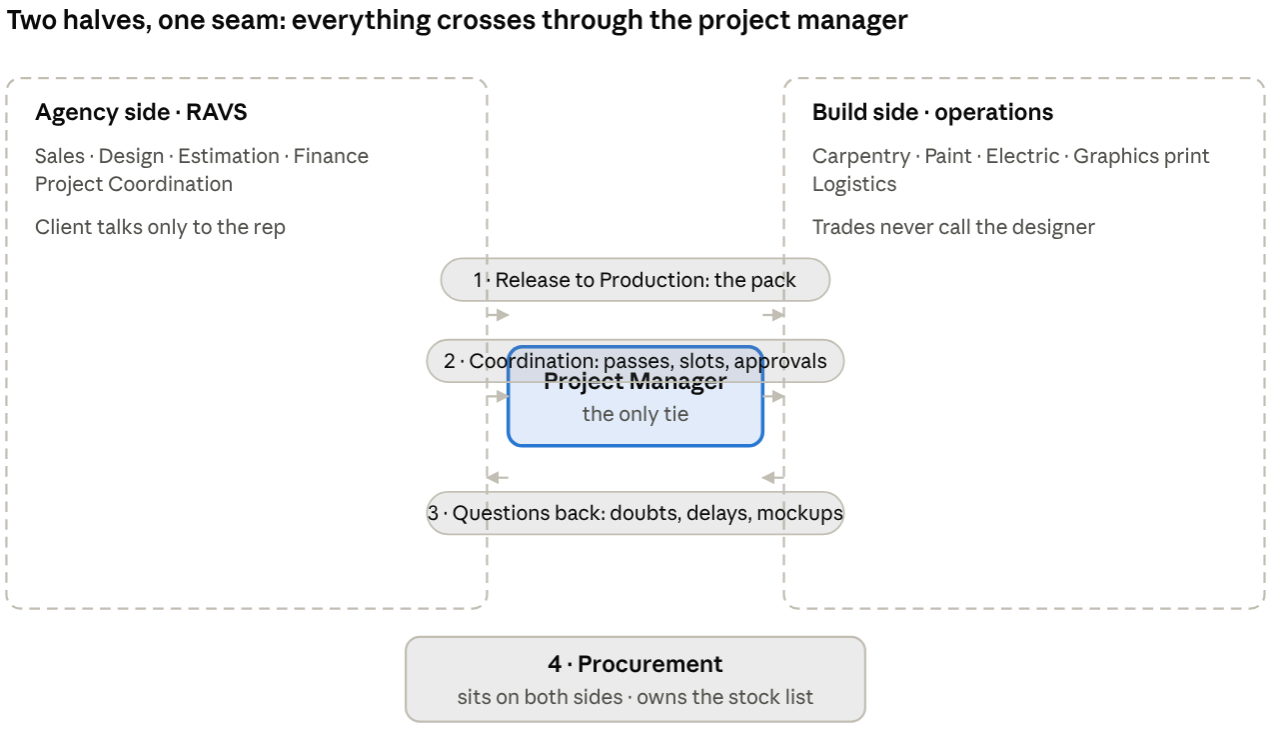


the seam · 3 flows through the PM, 1 shared department

Three flows pass through the project manager: the handover pack in, the coordination feed in, and questions back out. Procurement is the one department that lives on both sides.

The whole workflow, lead to dismantle

Whole workflow: agency wins and designs, PM releases, build side makes and delivers

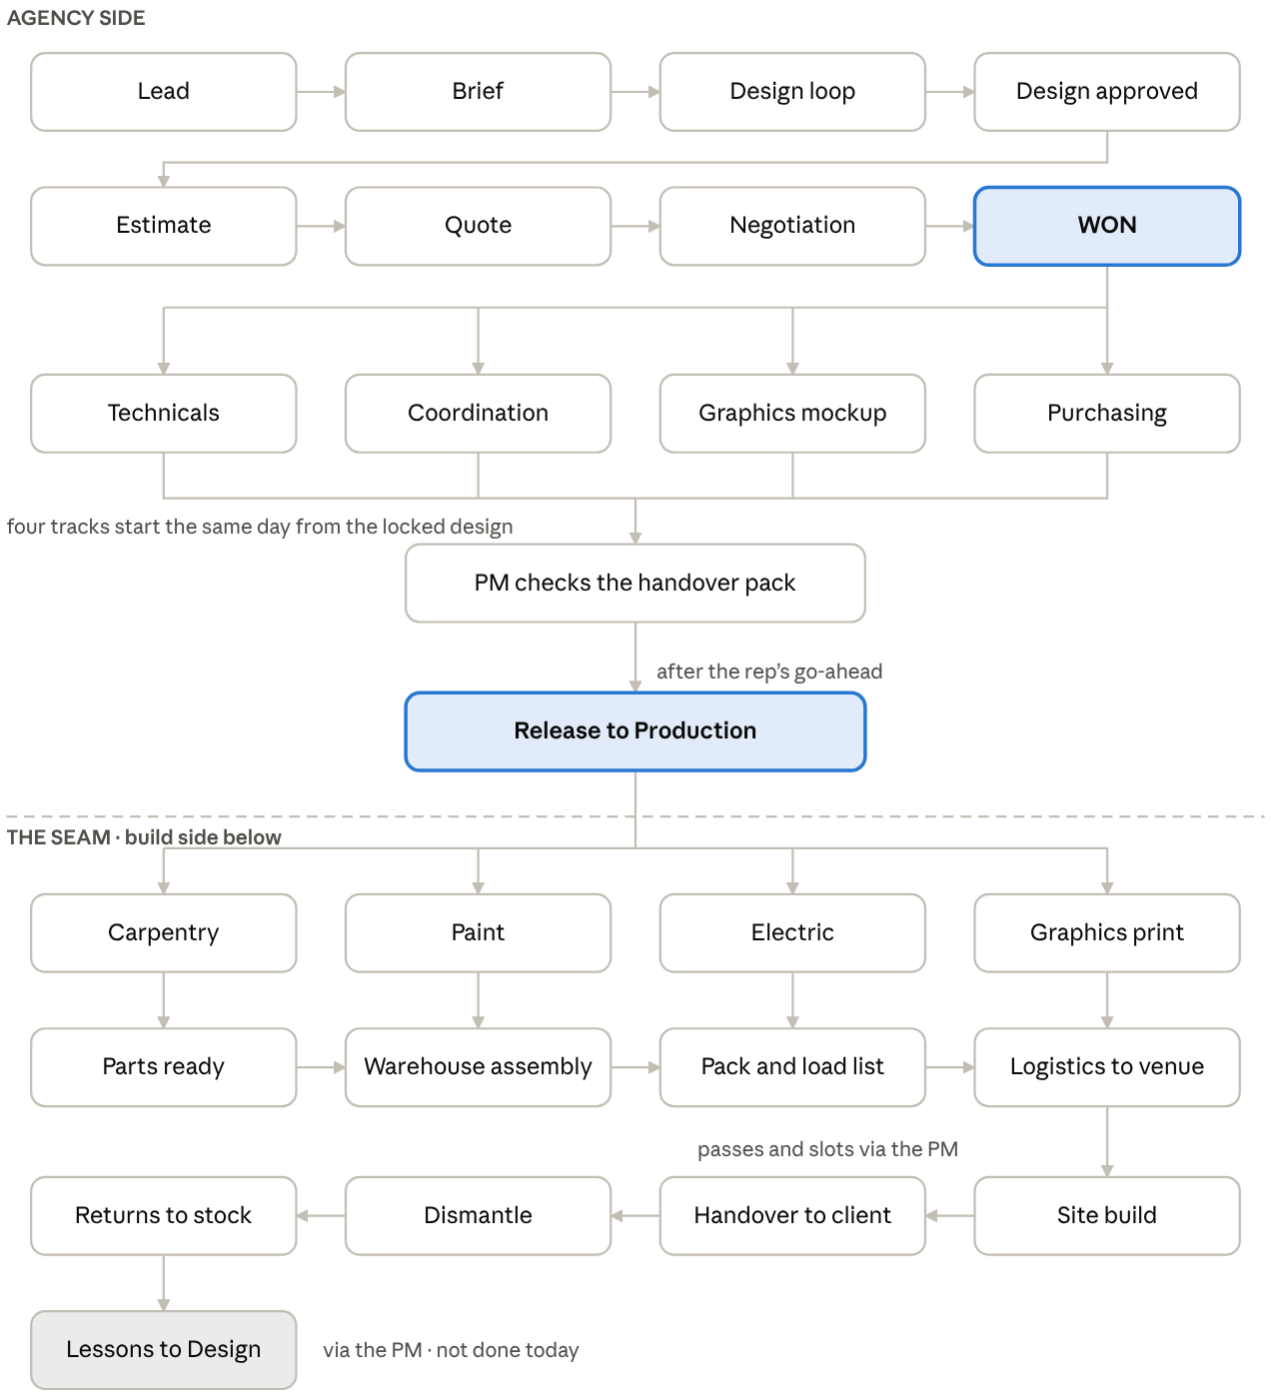

whole workflow · lead to dismantle, seam marked

Above the seam is the agency map in short. Below it is the build side as drawn on the department-flow map, with its own detail owned by operations: who hands what to whom between the trades, how the load list is built, and what logistics needs on site. The one loop that closes the whole thing, site lessons back to Design through the PM, does not exist today and is the first thing the two systems should add once both are live.

The four joints

Joint	Direction	What crosses	Through
1 Release to Production	Agency to build, once	The handover pack: locked design, approved technicals, print proofs, finish spec, build-affecting approvals, purchasing list. Timestamped by the PM after the rep's go-ahead	Project manager
2 Coordination feed	Agency to build, ongoing	Venue slots, gate passes, organiser and venue approvals as they land through the show	Project manager, then down to Logistics
3 Questions back	Build to agency	Measurement doubts, delays, shortages, mockup ready, anything that needs the client's answer	Project manager, then the rep if the client is needed
4 Procurement	Both sides	Reads the render at Won to split stock, reusable asset, and new to buy; issues stock and materials through the build; owns the stock list	Itself, as the one shared department

On the build-side map, joint 1 is arrows 1 to 5 collapsed into one gate; joint 2 is arrows 3 and 16 rerouted through the PM; joint 3 is arrows 8, 18, 20 and 21, all routed through the PM; joint 4 is arrows 6, 9, 10, 11 and 12.

Rules that keep the seam thin

- The client talks only to the rep. Changes and sign-offs never go from the client to the PM.
- Trades never call the designer. A doubt goes to the PM, who takes it to design.
- Project Coordination reports to the PM, not to Logistics. The PM passes slots and passes down.
- Procurement owns the stock list. Furniture is part of Procurement's inventory, not its own database.
- There is no per-stand BOQ. Procurement reads the 3D render.

- The graphic mockup and print proof are agency work under the Head of Design; the print itself is build work.
- Every approval is the login that pressed it; a client approval needs the client's message attached.

When the two maps disagree, the agency map rules for anything up to Release to Production and for the four joints above. The build-side map rules for everything inside the build.
