The stand file: what data exists, and who owns it

Proposal, not a design · nothing is built

One owner for each piece, so nobody keeps a second copy. Based on what Ali, Prateek, Bashini and Adhiraj told us; every row is a proposal to test with the people who do the work.

#	Data	What is in it	Owner (one)	Updated by whom, when, how
1	**Stand and job record**	stand ID, show, client, space size, build-up, show and dismantle dates, rep, PM, overall status	Sales (rep) creates; Aman adds the PM	Once when the job is won; PM added at allocation
2	**Design set**	3D, 2D plan, item and AV list (what Build calls the BOQ), special elements, version number, current or replaced	Design	On every upload; each new version replaces the old one
3	**Colour and finish spec**	one line per coloured element: Pantone or 'match to render', finish type	Design (Prateek's Build Spec)	Before release; any change is a change record
4	**Artwork, sizes and print proof**	artwork files, panel sizes, proof status, client approval, printed or not	Design (artwork and design mock-up); Branding (printed status)	Design uploads; rep records client approval; Branding taps printed, packed, fitted
5	**Item list and stock status**	each item: in stock, reusable or to buy; ordered; arrived; quantity	Design (item list); Procurement (stock status)	Design uploads list; Procurement updates status as it checks, orders and receives
6	**Handover pack and release**	checklist (technicals, colours, proofs, finish spec, approvals, purchasing list), rep's go-ahead, PM release time	PM	Pieces added by their owners; rep presses go-ahead; PM checks and releases
7	**Doubts**	stand, drawing, spot on the drawing, photo or voice note, who asked, answer, who answered, time	Raised by the trade; answered by Design	When a trade is unsure; Design answers on the same card
8	**Change records**	what changed, old and new version, why, who asked (Design, or the rep for a client change), who must see it, who has seen it	Design (design changes); the rep (client change orders)	Created at the moment of change; each department taps Seen
9	**Task status**	per stand and department: not started, working, done, blocked, with time and person; site steps (truck reached, offloaded, platform, electric, structure, putty, paint, fitting, logo)	Each department for its own tasks	One tap per task or step, at the Build area and on site
10	**Photos**	mock-up, finish, test, packed, site, snags; each tied to a stand and a step	Whoever does the step	A photo button on the task
11	**Show dates, passes and approvals**	build-up windows, loading-bay slots, gate and vehicle passes, organiser and venue approvals	Project Coordination	Entered once by Coordination; PM passes on to Transport
12	**Load list, crates and truck status**	items per crate, crate labels, scans at loading and offloading, truck booked, left, reached, offloaded	Transport at loading; trades list what they pack	Trades build the list; Transport scans; the PM sees the result
13	**Furniture and stock allocation**	which furniture and stock each stand uses; ready or short; returns	Procurement (Furniture is part of its inventory)	Procurement updates; the PM arranges with Transport (Narendra)
14	**People and equipment (later)**	head count per stand per day, own and outside; lights, cables and AV: where they are	Each foreman; Electric for equipment	One count a day per stand; equipment scanned out and in
15	**Site steps, snags, sign-off and lessons**	walk checklist, snag list, client sign-off, site changes for the invoice, three-tap lessons at close	PM	PM and trades tap on site; rep records the client's sign-off; PM taps lessons at close

Who updates it, and who uses it

Proposal, not a design · nothing is built

Read across a row: who creates it, who adds to it, who only reads, and who must tap Seen when it changes.

	Design	Sales & Finance	Procurement & Estimation	Project Coord.	PM	Aman	Production Coord.	Carpentry	Water Paint	Spray Paint	Electric	Branding (Print, Acrylic, CNC)	Transport	Top managers
1 Stand and job record		O		R	R	U	R	R	R	R	R	R	R	R
2 Design set	O	R	R	R	R	R	R	Seen	Seen	Seen	Seen	Seen		
3 Colour and finish spec	O	R			R			R	Seen	Seen		Seen		
4 Artwork, sizes and print proof	O	U			R			R			R	U		
5 Item list and stock status	O		U		R		R	R	R	R	R	R	R	
6 Handover pack and release	U	U	U	U	O	R	R	R	R	R	R	R		R
7 Doubts	U				R	R		U	U	U	U	U		
8 Change records	O	U	R		R	R	R	Seen	Seen	Seen	Seen	Seen	R	
9 Task status	R	R	R		R	R	U	O	O	O	O	O	O	R
10 Photos	R	R			U	R	U	U	U	U	U	U	U	R
11 Show dates, passes and approvals		R		O	R	R	R						R	
12 Load list, crates and truck status			R		R	R	R	U	U	U	U	U	O	
13 Furniture and stock allocation			O		R								R	
14 People and equipment (later)					R	R	U	U	U	U	U	U	U	
15 Site steps, snags, sign-off and lessons	R	U			O	R		U	U	U	U	U		R

O owns and updates **U** updates a part **R** reads **Seen** reads and must tap Seen when it changes (blank = not needed). Procurement, Estimation, Coordination, Sales, Finance and Design are Agency: shown because Build depends on them.

Stage by stage: what is made, what is needed, who is told

Proposal, not a design · nothing is built

The numbers in brackets point to the data on the first page.

Stage	What happens	Data made, and by whom	Data needed, and from whom	Who is told
0 Sell (Agency)	Lead, brief, design loop, estimate, quote, WON	Rep: stand and job record (1). Design: design set (2), colour spec (3), artwork (4), item list (5). Estimation: quote	Aman could see the likely stands by week now (idea: a pipeline view), so load is not a surprise	Nothing reaches Build yet
1 Release	Handover pack checked; rep says go; PM releases	PM: pack and release (6). Coordination: dates and approvals (11). Procurement: purchasing list. Design: final set	Every department sees only its part with NEW and taps Seen; PM sees who has not	Alert to each department with a link
2 Build area: start	Carpentry and Branding start; parts ready, Paint and Electric join	Each trade: task status (9), photos (10). Procurement: stock status (5). Trades: doubts (7)	Procurement answers 'is it in stock' to the PM and trades from the same record	Alert when a part is ready for the next trade
3 Build area: mock-up	Stand mock-up; graphic and logo mock-up; print proof	Carpentry, Paint, Electric: done taps and photos. Branding: printed. Rep: client approval (4). Design: changes (8)	Any change reaches every department on the stand with a Seen tap	Alert on change; red on the PM board until seen
4 Pack and move	Dismantle, label, load list; trucks booked	Trades: load list (12). Procurement: furniture and stock allocation (13). PM: ready to load. Transport: truck booking and scans	Transport reads the list and the dates; the PM reads truck status	Alert to Transport when a stand is ready to load
5 On site: build-up	Truck reached, offload, platform, electric, structure, putty, paint, fitting, logo	PM and trades: site steps (9, 15), photos, doubts (7), head count (14). Rep: client changes (8)	Foremen can see the current drawing without the PM; the PM sees steps from phones	Alert when a step is late against the usual time
6 Show and handover	Walk-through, snags, sign-off, daily checks	PM: snags and sign-off (15). Trades: snag fixes. Rep: client's sign-off	Sales and the top managers read status instead of receiving messages	Alert to the rep when snags are closed
7 Dismantle and return	Dismantle, scrap and keep, return to stock	Transport: crate scans back (12). Procurement: stock updated (5, 13). Electric: equipment back (14)	Procurement sees what came back without a call	Alert to Procurement when items return
8 Close	Handover sheet, final invoice, lessons	PM: closing sheet, lessons (15). Rep and Finance: change records feed the final invoice (8)	Design reads the lessons through the PM	Alert to Design with the lessons

Who puts data in, and who needs it, at each stage

Proposal, not a design · nothing is built

Green triangle up = makes or updates the data. Blue triangle down = needs or reads it. Each stand goes through these stages left to right.

	0 Sell	1 Release	2 Build area start	3 Mock-up	4 Pack and move	5 On site	6 Show, handover	7 Dismantle	8 Close
Design (Agency)	▲ design set, colours, artwork, item list	▲ final set	▼ doubts ▲ answers	▲ changes		▲ answers to doubts			▼ lessons
Rep (Agency)	▲ job, quote	▲ go-ahead		▲ client approval		▲ client changes	▲ sign-off ▼ status		▼ changes for invoice
Procurement (Agency)	▼ render, item list	▲ purchase list	▲ stock status		▲ furniture, stock allocated			▲ stock updated ▼ returns	
Coordination (Agency)		▲ dates, approvals, passes			▲ slots, passes (via PM)	▲ venue changes			
PMs		▼ pack ▲ release	▼ status	▼ mock-up photos	▲ ready to load	▲ steps ▼ truck status	▲ snags, sign-off		▲ lessons
Aman, Production Coord.	▼ pipeline	▲ PM, outside labour	▼ load	▼ load	▼ load	▲ head count			
Carpentry		▼ design set	▲ done taps ▼ item list	▲ mock-up photos	▲ pack list	▲ steps		▲ dismantled	
Water and Spray Paint		▼ colour spec	▲ done taps	▲ finish photos		▲ site painting			
Electric		▼ plan, AV list	▲ done taps	▲ test photos		▲ test, power on		▲ equipment back	
Branding (Print, Acrylic, CNC)		▼ artwork, sizes	▲ printed, cut	▲ proof fits	▲ packed	▲ fitted			
Transport					▼ pack lists, dates ▲ truck booked	▲ reached, offloaded		▲ returns scanned	
Top managers	▼ board	▼ board	▼ board	▼ board	▼ board	▼ board	▼ board	▼ board	▼ board

What each department updates and uses (1 of 2)

Proposal, not a design · nothing is built

Updates = what they put in, when and how (taps and photos). Uses = what they need from others. Used by others = who reads their data.

Carpentry

Foreman, 3 senior carpenters, 21 carpenters (HR chart)

UPDATES Task status per part (done, blocked) · photos of mock-up, structure and packed stand · doubts with a mark on the drawing · pack list for the load

USES Design set and changes (from Design) · item list and what has arrived (from Procurement) · sizes from Branding · ready-to-load date (from the PM)

USED BY OTHERS PM and Aman read progress without asking. Paint and Electric see 'parts ready'. Transport reads the pack list. Branding reads sizes

TYPING SAVED PM writing Carpentry's progress for them; 'is this the latest drawing?' calls

NOT KNOWN YET Who does metal; who leads the three seniors; who gives the daily work (PM or Production Coordination)

Water Paint

9 water painters; head not named (HR chart)

UPDATES Task status per part · photo of the finish · colour used (a tap on the spec line) · site painting on the same card · doubts

USES Colour and finish spec per element (Design) · 'part ready for paint' (Carpentry) · colour changes as change records

USED BY OTHERS PM and Aman see progress and paint work on site. Spray Paint sees which parts are theirs. Branding sees paint order

TYPING SAVED Asking for colours; repaint after a late colour change

NOT KNOWN YET Who leads; how paint use is recorded; how Water and Spray share one stand

Spray Paint

3 including the head (HR chart)

UPDATES Task status per part · spray area booked · photo of the finish · rare site work

USES Colour and finish spec · 'part ready' from Carpentry · changes

USED BY OTHERS PM and Aman see load on the spray area; Water Paint sees order

TYPING SAVED Same as Water Paint; the booth schedule on paper

NOT KNOWN YET How often they go on site and who decides; what limits the spray area

Electric

Foreman, 1 senior, 5 electricians; AV and lighting outsourced (HR chart, told)

UPDATES Task status (fit, test, power on) · test photo · equipment list per stand · outside AV and lighting booked (who, when) · doubts

USES Electrical and AV plan, item list · 'parts ready' · changes · venue power details (Coordination via the PM)

USED BY OTHERS PM sees on-site electric status without walking; outside AV companies could see their own stands; Procurement sees equipment needs

TYPING SAVED PM chasing electric status; the paper test notes

NOT KNOWN YET Who books outside AV and lighting; how equipment is tracked after the show

What each department updates and uses (2 of 2)

Proposal, not a design · nothing is built

Transport, the PMs, Aman with Production Coordination, and the Agency touchpoints.

Branding: Printing, Acrylic, CNC

Head and 5 (HR chart); Logo assumed to be acrylic

UPDATES Printed, packed, fitted per panel with photo · size check at 'printed' · CNC cut done · acrylic and logo done · doubts on measurements

USES Artwork zip, sizes and print proof (Design) · client approval (rep) · panel sizes from Carpentry · lightbox needs from Electric · changes

USED BY OTHERS PM reads panel status; Carpentry reads CNC output; Transport reads the pack; the rep sees proof status

TYPING SAVED Getting the zip by chat; asking Design about measurements; printing twice

NOT KNOWN YET Whether the mock-up approval is Design's or theirs; where Logo sits

Transport (Logistics)

Head and 6 drivers and loaders (HR chart)

UPDATES Truck booked, left, reached, offloaded (by scan or tap) · crate scans in and out · load list checked · return load

USES Pack lists (trades) · show dates, slots and passes (via the PM, from Coordination) · furniture and stock to load (Procurement, via the PM) · ready-to-load

USED BY OTHERS PM reads truck status; trades see what is missing; Procurement sees returns

TYPING SAVED 'Where is the truck?' calls; paper load lists

NOT KNOWN YET Who plans the trucks; owned or hired vehicles; whether they work on site

Project managers (3 plus Aman)

Each PM owns stands

UPDATES Release (6) · handover pack check · site steps and snags (15) · sign-off · lessons · what the client asked (to the rep) · ready-to-load · passes passed to Transport

USES Everything above: the board is built from the others' taps, so the PM types almost nothing

USED BY OTHERS Aman, the top managers and the rep read the PM's board and status page. Design reads lessons. Transport reads dates

TYPING SAVED Per-PM Excel, WhatsApp updates to Sales and the boss, relaying doubts and dates

NOT KNOWN YET How many stands per PM; what Aman needs on one screen

Aman and Production Coordination

Aman allocates; Production Coordination sits between the PMs and the divisions (2 people)

UPDATES Aman: PM allocation (1), outside labour and outside PMs · Production Coordination (if they allocate daily work): head count per stand (14) and which team is on which stand

USES Load board (derived), late alarms, pipeline from Sales, show dates

USED BY OTHERS Top managers read Aman's load; HR and Finance could read head counts later

TYPING SAVED Counting people by hand; guessing load

NOT KNOWN YET What Production Coordination actually does (Question 96)

Agency touchpoints (Prateek's side)

Design, the rep, Procurement, Coordination

UPDATES Design: design set, colour spec, artwork, changes, doubt answers · Rep: job, go-ahead, client approval, client changes · Procurement: stock and purchase status, furniture · Coordination: dates, passes, approvals

USES From Build: status, photos, doubts, site changes, lessons

USED BY OTHERS The PM reads all of it; trades read their parts

TYPING SAVED Forwarding files by chat; telling each department a change

NOT KNOWN YET Where the latest design lives (Decision A)

Built from taps, and how the brochures fit

Proposal, not a design · nothing is built

Nobody types the boards. The three brochures give us Ravashing's own names for items, materials and machines.

Views nobody types

View	What it shows	Built from
PM board	every stand: who has seen what, open doubts, last photo, late alarm	Built from tasks (9), changes (8), doubts (7), photos (10). The PM types nothing
Load board	stands per PM and per department by week; crowded weeks; shared machines (CNC router, spray area)	Built from stand records (1) and tasks (9); pipeline from quotes shows next weeks early
Top managers' board	stands by colour, next shows, risky stands (late, many changes, many doubts)	Built from the same records; no one writes a report
Sales status page	what the rep tells the client: steps done, photos, open snags	Built from tasks and photos; replaces messages upward
Late alarm	a step not done within the usual time after the one before it	Built from time stamps; the first version learns the usual times from the first stands
Lessons	reasons recorded in three taps at close, grouped by cause, sent to Design through the PM	Built from tasks, changes and doubts of a stand

The brochures as one chain (idea)

Design element
57 in 8 sections: logos, walls, paint, flooring, lighting, graphic and print, AV, other tech. Relative cost 1 to 5.

→

Materials
61: carpentry 11, paint 4, acrylics 4, metals 8, graphics 10, electricals 12, AV 5, truss and rigging 7. Thickness or width.

→

Machines
45: carpentry 12, metal 4, acrylic 5, printing 4, paint 5, assembly 6, electrical 2, handling and installation 7.

If Design's item list uses these names, three things follow: Procurement matches items to stock without guessing; Estimation can price them; and each element shows which machines it needs, so Aman sees the CNC router or the spray area filling up before it happens.

Assumed until we check whether item lists use these names (Question 101). The brochures carry no prices.


Still not known

- What Production Coordination (2 people) does and writes down
- Who does the metal work; who leads the three senior carpenters
- Where the latest design lives, and where doubts go first
- Phones, languages, venue Wi-Fi
- What each top manager wants to see

One stand, from go-ahead to the show floor

Concept, not a design · nothing is built · fictional example data

Ravashing Exhibitions & Events · 6 Nov 2026 · Confidential. How a stand could move through one portal. WhatsApp stays as the doorbell (a short alert with a link); the work and the history live in the stand file.

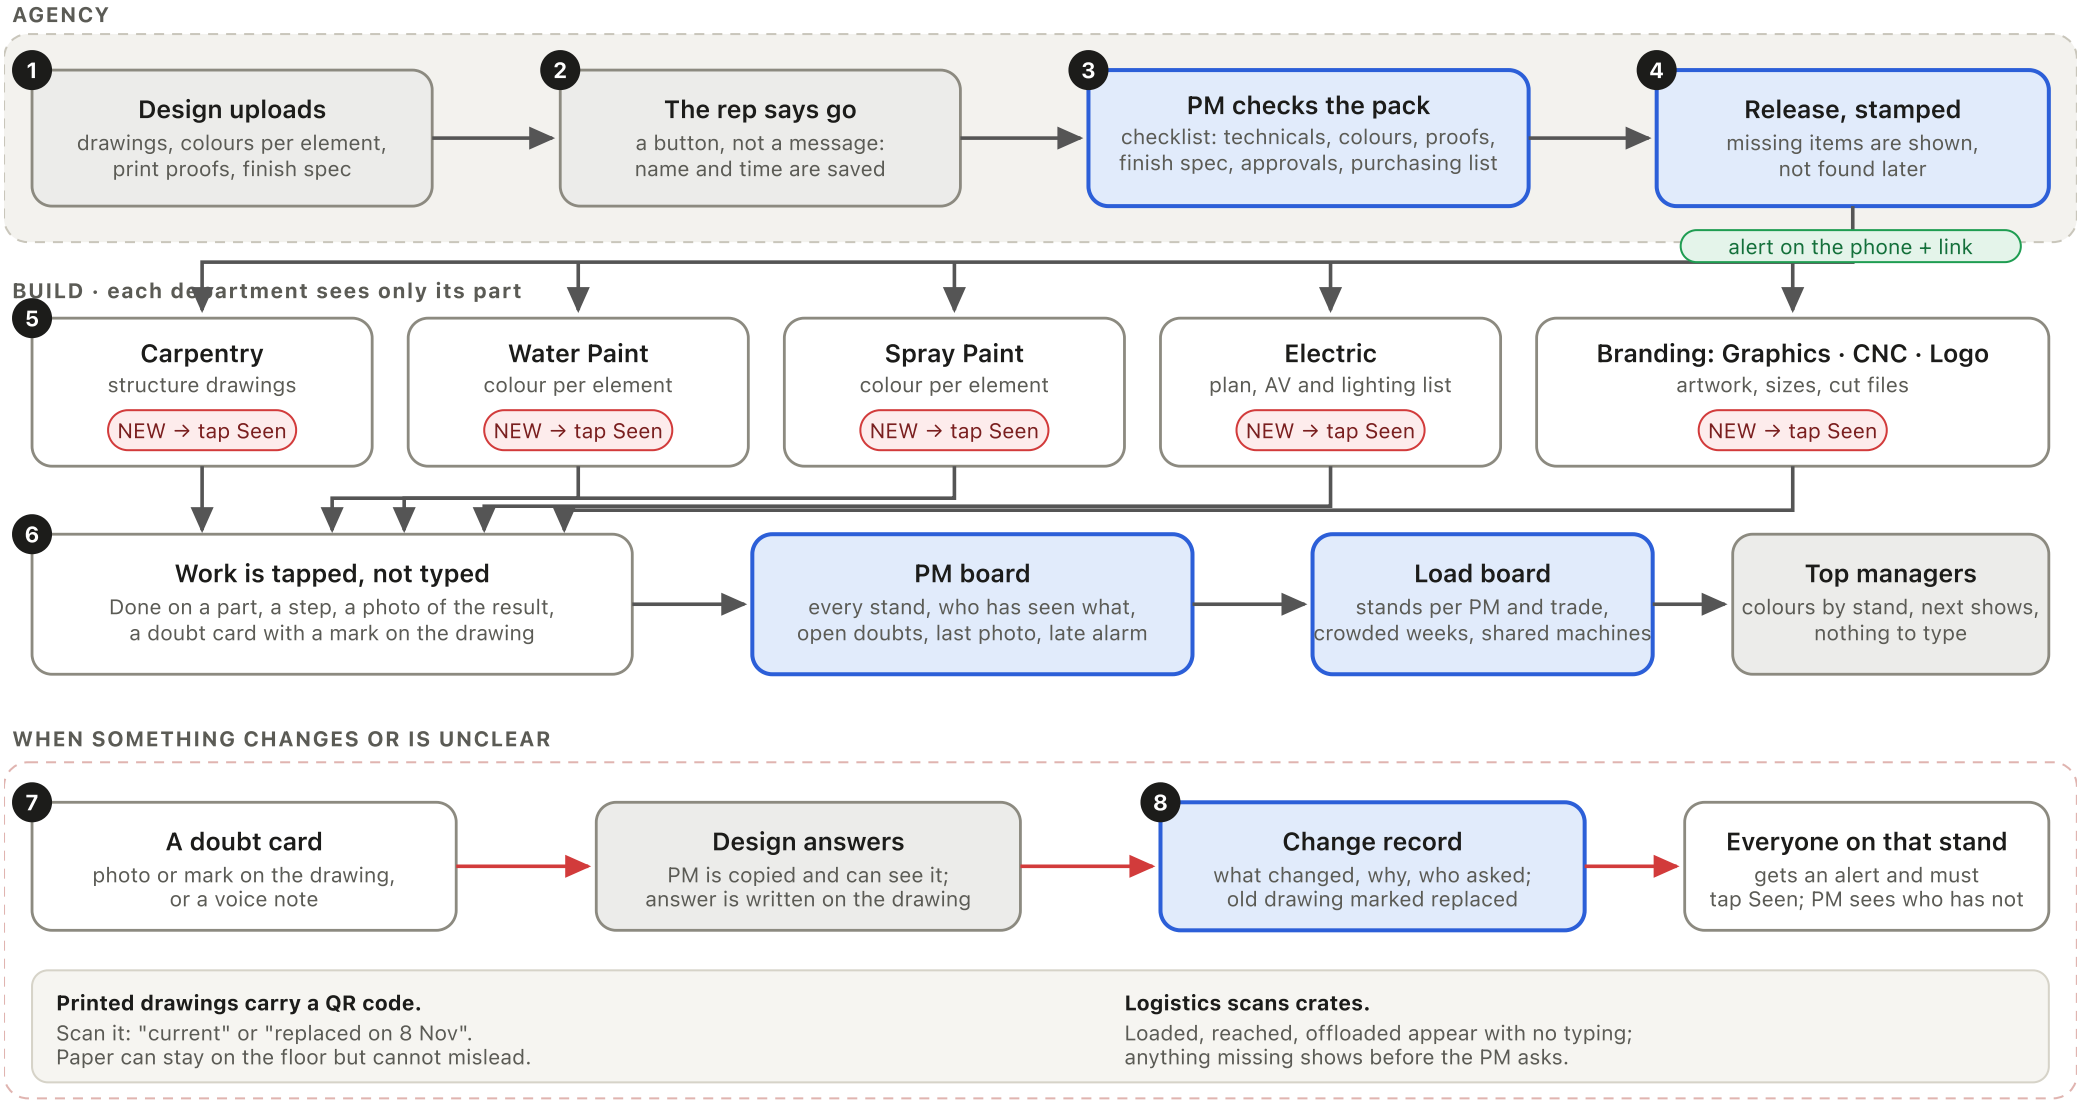

Printed drawings carry a QR code.
Scan it: "current" or "replaced on 8 Nov".
Paper can stay on the floor but cannot mislead.

Logistics scans crates.
Loaded, reached, offloaded appear with no typing; anything missing shows before the PM asks.

What each person would see

Concept, not a design · fictional example data

Six screens, drawn as rough sketches. Big buttons, almost no typing. Every name, stand and number below is made up.

Foreman or worker: "My stands"

Carpentry · phone

Design changed Fri 17:02. Panel B is 20 mm narrower. Seen

- **Stand A-12** · build panels due Wed — Done
- **Stand B-07** · frame due Fri — Photo ?
- **Stand C-03** · packed photo added

Tap "?" to raise a doubt on the drawing. Tap Done to mark a part. No typing.

PM: "My stands"


Project Management · phone or screen

- **A-12** · Carpentry has not seen the change — Nudge
- **B-07** · 1 doubt waiting for Design
- **C-03** · packed, truck booked
- **D-21** · colours missing in pack

On site: a step checklist per stand (truck reached, offloaded, platform, electric, structure, paint, logo). One tap each; the time is saved.

Head of PMs: load board

Weeks across, PMs down · screen

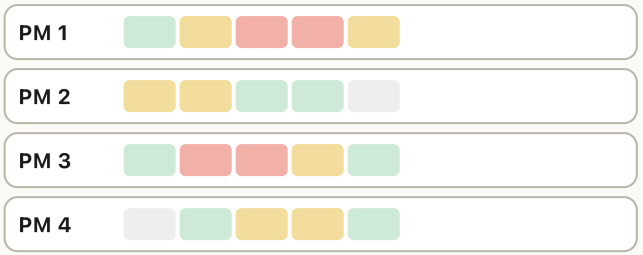

Red = too many stands that week. A flag appears when two stands want the same machine or the spray booth in the same week.

Top managers: the board

Nothing to type · screen

- **Show 1** · 6 stands — 5 on track
- **Show 2** · 9 stands — 2 late, 4 changes
- **Show 3** · 4 stands — colours missing

Risky stands rise to the top: late, many changes, many doubts. Replaces the status messages sent upwards.

Branding: the print list

Graphics · CNC · Logo · phone or screen

- **Panel B, 2400 × 900** size matches current drawing? — Yes No
- **Logo, level 2** · printed — Packed
- **CNC cut: bracket set** — Photo

The size question at "printed" catches a panel made to an old size before it is packed. The artwork and cut files arrive in one place.

Logistics: the load list

Loading bay · phone

- **Truck 2 · Show 2** · 31 of 34 loaded — Scan
- 3 crates not scanned: Stand D-21
- Furniture for A-12 · loaded

Scanning a crate marks it loaded. At the venue the same scan marks it offloaded. The PM sees "truck left, reached, offloaded" without a message.

Not shown: Electric and Paint screens look like the foreman's (a list of stands, a Done tap, a photo, a doubt). Electric adds a test checklist; Paint adds the colour per element.

What changes, and what we need to decide

Concept, not a design

From the lists of lags and wasted effort in IMPROVEMENT_IDEAS.md. Most "today" items are what we were told, and are not yet confirmed.

Today	With the portal
Handover arrives in pieces: email, WhatsApp. Nothing says "released".	One checklist, one release stamp.
A design change reaches some departments, not others.	Change record; each department taps Seen; the PM sees who has not.
Printed drawings go stale.	QR on the paper shows if it is current.
Colours chased from the client mid-build.	Colour per element is part of the pack before release.
Site status typed in WhatsApp; one Excel per PM.	One tap per step. One shared stand list.
PM retypes status for Sales and the top managers.	They read the board.
Photos scattered in chats.	Photos stay on the stand and the step.
Doubts go by phone to Design or the PM.	A doubt card; answer written on the drawing for everyone.
Truck and load questions by call.	Crate scans show loaded, reached, offloaded.
Nobody sees load or lateness early.	Load board and late alarm.

Decisions for Prateek and Narendra

1. **Where does the latest design live?** In Prateek's system or ours. We must keep one copy only; ours should link to his.
2. **Doubts:** through the PM first, or to Design with the PM copied? The first may overload PMs on site.
3. **Foremen's progress:** may foremen tap their own progress, instead of the PMs keeping it for them?
4. **Devices, languages, Wi-Fi:** phones or a shared tablet? Which languages? Venue Wi-Fi may fail, so site use must work offline.
5. **Outsiders:** may outside labour, AV and lighting companies, or hired trucks see a limited view?
6. **Alerts:** WhatsApp, SMS or an app alert, and what the approved-tools list allows.

Where I would start

PMs, Carpentry and Branding, with one idea only: **one current design, and who has seen it**. Test it on two or three real stands. Habit is the main risk, not code.
